

Redwood Coast Montessori School

REQUEST FOR QUALIFICATIONS REQUEST FOR PROPOSALS

Heat Pumps & Solar Photovoltaic System

Date Issued:
April 25, 2022

Redwood Coast Montessori School Contact:

Bryan Little, Director
Redwood Coast Montessori School
1611 Peninsula Drive, Arcata, CA 95521

Phone: (707) 832-4194
Email: bryan@redwoodmontessori.org

Project Manager Contact:

Patricia Terry, Project Manager
Redwood Coast Energy Authority
633 3rd Street, Eureka, CA 95501

Cell Phone: (707) 382-2098
Email: pterry@redwoodenergy.org

**Pre-Proposal Site Visit on Tuesday, May 3rd at 11:00 am
at Redwood Coast Montessori School, 1611 Peninsula Drive in Manila, CA.**

**Proposals Due on Friday, May 13, 2022, at 3:00 pm at
633 Third Street
Eureka, CA 95501**

TABLE OF CONTENTS

Request for Qualifications and Request for Proposals

	Introduction and Overview	3
	Statement of Work	4
<u>APPENDICES</u>		
Appendix A:	Proposed Project Schedule	8
Appendix B:	Proposal Response Requirements	9
Appendix C:	Energy Services Contract	14
Appendix D:	Performance Bond	59
Appendix E:	Payment Bond	61
Appendix F:	Warranty Bond	63
Appendix G:	Subcontractor List	65
Appendix H:	Technical Facility Profile	66
Appendix I:	Floor Plan	67
Appendix J:	Site Plan	68

REQUEST FOR QUALIFICATIONS/ REQUEST FOR PROPOSALS

Heat Pumps and Solar Photovoltaic System

Redwood Coast Montessori School (School)

INTRODUCTION

Redwood Coast Montessori School (School) solicits proposals responsive to this Request for Qualifications/Request for Proposals from interested Energy Service Companies (ESCOs) to design, permit, install and commission both a fully integrated and operational solar photovoltaic (PV) system and heat pumps for the classrooms to replace existing propane furnaces. A proposed schedule indicating the timeline for this solicitation is identified in **Appendix A: Proposed Project Schedule**. A pre-proposal site visit and question forum will be held on **Tuesday, May 3** at 11:00 am at Redwood Coast Montessori School, 1611 Peninsula Dr, Arcata (Manila), CA 95521. The site visit and forum are designed to increase the likelihood that respondents have the applicable and appropriate information necessary to deliver proposed solutions that meet the School's expressed needs. Since school will be in session, it is requested that all attendees wear facial coverings.

OVERVIEW

This solicitation seeks proposals for installation of heat pumps and a Photovoltaic (PV) system to be located on property owned by the School at 1611 Peninsula Dr, Arcata (Manila), CA 95521. **The expected work product will be to remove seven (7) existing gas heaters, design and install heat pumps, and design and implement a roughly 10.2 kW DC solar photovoltaic (PV) array that has a first-year production value of approximately 12,632 kWh. ESCO will design a system that will be interconnected under PG&E's current Net Energy Metering (NEM-2) program and be capable offsetting the additional electrical load from the heat pumps.** The school has an existing 16.5 kW DC solar array with an existing NEM agreement, a variance from PG&E for a second NEM interconnection may be required. The potential array location is a single-story structure with a composite shingle roof providing a large south facing installation area as described in **Appendix H: Technical Facility Profile**. However, proposers may also consider alternate locations on other School buildings. **Total allocated ECAA-Ed funding available to the School for this project, including permitting and design, is \$155,926.00.** ESCO's submitting proposals are being asked to provide plans for design and installation of a system that would incorporate this funding. School is requesting assurance that the ESCO can execute an interconnection agreement with PG&E for this project under the current NEM-2 rules. The selected ESCO will work with the School to determine the best installation option/location(s), considering initial installation costs, long-term maintenance and operational costs, technical feasibility, permitting restrictions, aesthetics, customer preferences and future facility upgrades.

As an additive alternate, the ESCO should propose a design for adding ventilation to the facility. A ducted heat pump system with outside air or energy recovery ventilation are some options. If budget allows, this additive alternate may also be funded by the ECAA-Ed loan.

This procurement for design build services is authorized as an energy service contract pursuant to Government Code section 4217.12. Prior to the potential award of a contract to the selected ESCO, the School Board of Directors will adopt a resolution as required by Government Code section 4217.12, finding that the anticipated cost to the School for electrical power generation to be provided by the proposed solar power project will be less than the anticipated marginal cost to the School of electrical energy that would

have been consumed by the School in the absence of this project. The contract with the selected ESCO will be the sole contract the School will hold for the completion of this project.

STATEMENT OF WORK

The scope of services provided by the selected ESCO shall include all tasks required to design, fabricate, store, deliver, install, and commission a fully operational Heat Pump and PV system for the School. Any required ancillary equipment, such as security fencing for a ground-mounted installation, or access ladders for roof-mounted panels, are included in the scope of work. The scope shall also include, but not be limited to, securing all permits and approvals from governing agencies, all labor, taxes, services, permit fees, training, and equipment necessary to produce a fully operational Heat Pump and solar PV system.

The selected ESCO will be expected to work with the School to design/engineer the solar PV and Heat Pump systems to meet the School's specific design and funding criteria, and to maximize the solar energy resources, taking into consideration the School's electrical demand and load patterns, proposed installation site, available solar resources, existing site conditions, proposed future site improvements, and other relevant factors. In addition, the selected ESCO will be expected to complete installation and integration of the systems based on a schedule as dictated by the School's funding sources for this project.

The selected ESCO will:

1. Design, Procure, Install, Test, and Commission a Grid-tied Solar PV System.
 - a. Provide all design, labor, and materials for a turnkey, code compliant installation of a 10.2 kw (DC) grid tied solar photovoltaic array, or similar sized array, capable of producing 12,632 kWh /year.
 - b. The system shall be designed to interconnect under PG&E's Net Energy Metering (NEM-2) program and offset the estimated additional electrical load from the heat pumps. School is requesting assurance that the ESCO can execute an interconnection agreement with PG&E for this project under the current NEM-2 rules.
 - c. PV array should be installed on the south facing roof of Building 2 – Classrooms and Multipurpose Room. **See Appendix H: Technical Facility Profile.**
 - d. Equipment
2. Provide and install all solar modules, rapid shutdown devices, grid-tied inverter, racking system, means of disconnect for all AC and DC components, and all other balance of system equipment, including conduit, conductors and over current protection devices required for a code compliant installation. Provide and Install heat pump and ventilation system in (6) classrooms and (4) other rooms.
 - a. See **Appendix I** for the Floor Plan of Redwood Coast Montessori.
 - b. Demolition
 - i. Remove existing propane furnaces and associated venting, gas lines and electrical.
 - ii. Ensure exterior roof or wall penetrations are properly sealed and insulated.
 - iii. Ensure gas lines are properly capped off outside of the classroom space and at Manila Community Service District's point of origin, if possible.
 - iv. Ensure proper disposal of the removed heating unit and associated equipment.
 - c. Mechanical
 - i. Provide all design, labor, and materials for a turnkey, code compliant installation of a heat pump system to replace existing propane heaters.

- ii. Heat pump system shall add outside air ventilation to the classrooms and multipurpose room, although existing systems may not include ventilation.
 - iii. Heat pumps in classrooms replacing an existing propane furnace that currently heats two classrooms should either be:
 - 1. Ductless mini-Split heat pump SEER 18 or greater with two (2) indoor units, one in each classroom with the existing shared furnace, and one (2) outdoor unit installed outside the classrooms.
 - 2. Or, unitary central split system heat pump that will fit in the existing furnace closet that can be ducted to the two classrooms.
 - 3. Or, other system to be specified by the proposer.
 - iv. Provide, run, and install necessary refrigerant lines and cover with line set covers. ESCO shall coordinate with District for approval on final location and layout of lines and line set covers,
- d. Install foundation for outside unit, level concrete pad 4 to 6 inches thick slightly above grade or use pre-engineering pad.
 - i. Outside unit should be properly secured to the new foundation.
 - ii. Provide and install protective/vandal proof caging around outdoor unit.
 - iii. Provide additional support as needed.
- e. Temperature Controls
 - i. Each heat pump should be controllable by a programmable and wi-fi enabled thermostatic control.
 - ii. Ensure proper operation of thermostatic zone control.
- 3. Provide and install all labor and materials for a code compliant installation of dedicated circuits and non-fused disconnect to serve new heat pumps.
 - a. See Appendix I for a Floor Plan.
 - b. Ensure penetration on the roof is weatherproof. Install roof flashing and seal as needed.
 - c. All conduits to be outdoor rated with weather tight connectors.
 - d. Provide support for conduit and disconnect as needed.
- 4. Permitting and reporting
 - a. Obtain all permits required for installation and interconnection of the PV system to the utility grid under the current NEM-2 rules. School is requesting assurance that the ESCO can execute an interconnection agreement with PG&E for this project under the current NEM-2 rules.
 - b. System must comply with 2019 Building Energy Efficiency Standards (Title 24, Section 6)
 - c. All project services will comply with Energy Conservation Assistance Act (ECAA) Guidelines.
 - i. The ESCO will provide any necessary data and coordinate the project with all ECAA-Ed submission and reporting requirements.
 - ii. The ESCO will coordinate with the School and Redwood Coast Energy Authority to ensure adherence to California Energy Commission ECAA-Ed Loan guidelines.
- 5. In addition to completing the scope defined above:
 - a. The proposal shall contain a detailed explanation of the complete project and delineation of all work tasks to be performed by the awarded ESCO. The proposer must have the technical capability and demonstrated experience to complete the project as set out in this RFP.

- b. The selected ESCO will be expected to furnish all electrical, structural, and mechanical designs and specifications that are requested and/or required by any other regulatory bodies with jurisdiction over the project.
- c. Installation of the system is subject to California prevailing wage requirements, and the selected ESCO and its subcontractors are required to pay all workers employed for the performance of this contract no less than the applicable prevailing wage rate for each such worker. This project is subject to compliance monitoring and enforcement by the California Department of Industrial Relations pursuant to Labor Code sections 1725.5 and 1770 *et seq.* In accordance with Labor Code sections 1725.5 and 1770 *et seq.*, all contractors and subcontractors working at the site shall be duly registered with the Department of Industrial Relations at time of bid opening and at all relevant times. Proof of registration shall be provided as to all such contractors prior to the commencement of any work.
- d. The selected ESCO will work with the School and its representatives to determine the best approach for design. Final scope approval will be given prior to installation.
- e. After approval of a final design by the School and the Project Manager, and after receiving any necessary regulatory approvals, the ESCO shall provide all necessary materials, equipment, and labor to construct and successfully commission the photovoltaic system installation and interconnection with the electrical grid.
- f. The ESCO shall provide approved training for designated School personnel in the operation of the entire photovoltaic system, including the operation and maintenance of inverters, transfer switches, panel board, disconnects, and other features as requested by the school. The ESCO shall provide the school with written instructions and procedures for shutdown and start-up activities for all components of the system. The ESCO shall also provide training on the Heat Pump system and provide written instructions for operation and maintenance.
- g. All equipment provided by the ESCO for this Project shall have a history of successful operating experience in similar installations and shall be in new, unused condition. This equipment shall be current technology with readily available non-proprietary replacement parts. All equipment used for this Project shall be approved by the School prior to installation.

Additive Alternate:

1. Design and Install ventilation system for classrooms. Either:
 - a. One (1) energy recovery ventilator (ERV) installed inside the existing furnace closet and ducted to provide fresh air to the two classrooms from a single inlet, or
 - b. Addition of fresh air ducts to ducted heat pump system, or
 - c. Other system as specified by proposer.
2. Provide and install all labor and materials for a code compliant installation of dedicated circuits and non-fused disconnect to serve new ventilation systems.

EXPECTATIONS

ESCO's duties shall include but may not be limited to the following:

- Prepare construction documents where necessary.
- If necessary, hire design professionals to create plans and specifications.
- Ensure compliance with governing codes and standards including, but not limited, to Title 24 Standards and the California Building Code.

- Ensure compliance with all requirements for photovoltaic installations contained in the National Electric Code (NEC) and the California Electric Code (CEC), including, but not limited to, Articles 250, 310 and 690.
- Ensure Compliance with Public Works contracting requirements, specifically involving prevailing wage and certified payroll records.
- Ensure compliance with ECAA requirements.
- Ensure the School participation and feedback in scoping process.
- Provide a schedule for completion of Project.
- Prepare a plan for ongoing equipment maintenance and system upgrade, if requested as an alternate.
- Ensure delivery of all materials and equipment to Site(s).
- Construct/Install Project.
- Manage all Subcontractors.
- Meet regularly to update the School representatives as to Project progress.
- Obtain and maintain all licenses, permits, and authorizations as needed for the Project.
- Commission Project: provide training on equipment/systems and monitoring if requested.
- Provide project closeout which may include As-Builts, operations and maintenance information with a training and monitoring session, permits, warranties and completion documentation.

APPENDIX A: PROPOSED PROJECT SCHEDULE

The following schedule is the proposed schedule and may change during the project.

ACTIVITY	DATE
Issue RFQ/RFP	Monday, April 25th, 2022
Pre-Proposal Site Visit	Tuesday, May 3 at 11 a.m.
Questions and Clarifications Due	Friday, May 6, 2022 by 5 p.m.
Answers to Questions and Clarifications Released	Monday, May 9, 2022 by 5 p.m.
Proposals Due	Friday, May 13, 2022 3:00 p.m.
Review and Selection of Finalist(s)	Friday, May 20, 2022
ESCO Selected/Notice of Award issued	June 16, 2022
Contract Finalized/Notice to Proceed issued	June 30, 2022
Conduct Design Work	July 2022
Build Project	July-August 2022
Construction Complete	no later than December 1, 2022
Project Close-out and System Commissioning	Dec 1, 2022 – Feb 1, 2023

APPENDIX B: PROPOSAL REQUIREMENTS

For further information, please contact:

Patricia Terry, Project Manager
Redwood Coast Energy Authority
633 3rd Street, Eureka, CA 95501

Cell Phone: (707) 382-2098
Email: pterry@redwoodenergy.org

PROPOSAL REQUIREMENTS

Please e-mail proposals to Patricia Terry pterry@redwoodenergy.org and cc: Marianne Bithell mbithell@redwoodenergy.org. Due to possible server delays, proposals should be e-mailed in advance of the deadline. **Late responses will not be accepted.**

Each proposal shall include the following information:

ESCO PROFILE & QUALIFICATIONS

The School may award the contract to the firm that, in its sole opinion, is the most capable of providing the range of services described in this RFP. To be considered for this Project, a proposer must, at a minimum, have demonstrated knowledge and experience in design, engineering, and construction capabilities relevant to the scope of this RFP. The proposal must contain a response to each of the following:

- *Answer all questions or state “N/A” if not applicable.*
 - *Please number and re-state each subheading or question, followed by your response. This improves clarity and makes it much easier to evaluate your response.*
 - *Number all pages.*
1. Name, address, contact numbers, email, website, and summary of the responding ESCO’s experience with public school projects and energy upgrades.
 2. If the responding ESCO is a business entity, provide information on the type of entity, its ownership, size, and location of its principal office.
 3. All applicable licenses including license numbers and expiration dates.
 4. Detailed resume(s) of personnel to be assigned to the Project.
 - a. Identify proposed sub-ESCO(s) by name, address, and work to be performed.
 - b. Summarize the scope of services (design, construction, training, etc.) directly offered by ESCO.
 - c. Describe your or your subcontractor’s qualifications and ability to design and install solar PV arrays.
 - d. Describe your or your subcontractor’s qualifications and ability to design and install heat pumps and ventilation systems.

- e. Please list any special certifications or training for heat pump and ventilation systems.
5. List at least three (3) applicable design and/or construction projects completed by the ESCO and proposed Subcontractors within the past five (5) years that are similar in size and scope. Identify similar projects by name, location, owner, size, and date constructed.
 - a. Include a list of references including contact names and telephone numbers for the representative projects.
 - b. Source of funds used for the project (if known).
6. Describe your general approach to designing and constructing building systems and how the School will be involved in the process?
7. Provide a preliminary implementation plan that includes but is not limited to:
 - a. Recommended location and required ancillary activities necessary to successfully install and grid-tie the proposed system.
 - b. Steps to ensure all applicable building codes and/or state requirements are met.
 - c. Steps to ensure all applicable labor compliance requirements are met.
 - d. Number of trainees and or apprentices to be used.
 - e. Proposed Installed kW.
 - f. Proposed First year kWh production values that meet or exceeds funding requirements.
 - g. Proposed Heat Pump and ventilation system including installation.
 - h. Total Installed costs that are equal to or less than the not-to-exceed amount.
 - i. Estimated first year energy cost savings.
 - j. Include a system monitoring service that can be used to retrieve such data for educational purposes.

The respondent may choose to use the following format to present project metrics.

<i>Size (kW DC)</i>	<i>Demand Savings (kW)</i>	<i>Year 1 Production (kWh)</i>	<i>Effective Useful Life</i>	<i>Year 1 Energy Cost Savings (\$)</i>	<i>Inverter Size (kW)</i>	<i>Measure Cost (\$)</i>

8. Confirm and briefly discuss labor, panel, and inverter warranties.
9. School encourages ESCOs to maximize production and system size while saying below the project not to exceed value.
10. Public works ESCOs and Subcontractors must be registered with DIR, as specified in Labor Code section 1771.1(a). Project is subject to compliance monitoring and enforcement by DIR.

11. Proposed Price

- a. The proposed price shall include all project costs (including design fees, bonding, insurance, engineering, permits, materials, labor, testing, commissioning, inspection, etc.).

Measure Description	Proposed Price
Design, Procure, Install, Test, and Commission a Grid-tied Solar PV System.	
Provide and Install heat pump in (6) classrooms and (4) other rooms	
Installation of dedicated circuits and non-fused disconnect to serve new heat pumps	
Additive Alternate: Provide and Install ventilation system	
Total Cost for all Measures	

ENERGY CONSERVATION ASSISTANCE ACT (ECAA) REQUIREMENTS

ESCOs will be required to comply with the ECAA requirements.

ESCO acknowledges that all work must qualify as an eligible project under the ECAA guidelines; and that the Statement of Work may be amended to reflect changes in funding allocation upon mutual agreement of the Parties and a written amendment to this Contract related to any changes in scope, payment, and duration. Prior to commencement of any Work, the School shall review and approve the Project.

The ESCO will comply with and give notices required by laws, ordinances, rules, regulations, and lawful orders of public authorities bearing on performance of the Work, including but not limited to data, quarterly reports and final reporting to the California Energy Commission required under ECAA.

COMPENSATION & PAYMENT

Compensation will have a not-to-exceed cap based on the estimated funding allocation for the approved project, and an agreement to modify (increase or decrease) the cap if ECAA funds change.

The payment schedule will be consistent with the funding allocation schedule. The ESCO will agree to maintain and make available records for inspection by the School and other agencies and will provide or assist the School in providing required reporting for the project, including data for reports to the ECAA Citizens Oversight Board.

AGREEMENT

The selected ESCO must enter into a written agreement for services using the School's form agreement for Energy Services (the "Contract"), a copy of which is included as **Appendix C**. The Contract includes the following indemnity requirement:

"ESCO shall indemnify, defend with counsel acceptable to Redwood Coast Montessori School, and hold harmless to the full extent permitted by law, Redwood Coast Montessori School, its governing board, officers, agents, employees, and volunteers from and against any and all liability, demands, loss, damage, claims, settlements, expenses, and costs (including, without limitation, attorney fees,

expert witness fees, and costs and fees of litigation) (collectively, “Liability”) of every nature arising out of or in connection with Consultant’s acts or omissions with respect to this Agreement, except such Liability caused by the active negligence, sole negligence, or willful misconduct of the Redwood Coast Montessori School. This indemnification obligation is not limited by any limitation on the amount or type of damages or compensation payable under Workers’ Compensation or other employee benefit acts, or by insurance coverage limits, and shall survive the expiration or early termination of this Agreement.”

SELECTION PROCESS

A selection committee will review the proposals and may select a short list of finalists for oral interviews.

REFERENCE CHECK

The School will conduct a background/reference check of the responding firms. Proposed ESCOs that appear to have the necessary qualifications and who are acknowledged as competent to provide the services requested may be placed on the short list of finalists and interviewed.

INTERVIEW

The School may interview selected respondents.

FINAL SELECTION

Predicated upon thorough review of proposals submitted and upon interviews with selected firms, the School will make a final selection and notify all finalists in writing.

The School will negotiate the final terms for services with the firm approved by the School Board. If it is not possible to reach mutual agreement with the designated firm, the School reserves the right to enter into negotiations with another firm.

The final selection will be made on the basis of best value, which includes, but is not limited to the following criteria:

- Completeness and adherence to the requirements of this RFP.
- Qualifications and past similar experience.
- References.
- Fee and rates and base price proposal.

The School reserves the right to postpone selection for its own convenience, to withdraw this Request for Proposal at any time, and to reject any and all submittals without indicating any reason for such rejection. Submitted proposals become the property of the School.

As part of the negotiation process, the School reserves the right to require correction of technical errors in the proposal and to modify the published Statement of Work and to approve or disapprove the list of sub-consultants. Should the School determine that specific expertise is lacking in the project team, the School will reserve the right to request specific consultants with specific expertise to be added to the team. Any interpretation of, or change in, this Request for Proposal will be made by addendum, and shall become part of the Request for Proposal and any contract awarded.

Note: Pursuant to Government Code section 4529.12, School employees are prohibited from participating in the selection process when they have a financial or business relationship with any private entity seeking to enter into a contract with the School, and the School requires compliance with all laws regarding political contributions, conflicts of interest or unlawful activities.

The School reserves the right to contract with any entity responding to this Request for Proposals. The School makes no representation that participation in the Request for Proposal process will lead to an award of contract or any consideration whatsoever. The School shall in no event be responsible for the cost of preparing any proposal in response to this Request for Proposals. The selection of ESCO(s) to participate in the Request for Proposal process if at all is at the sole discretion of the School.

From the period beginning on the date of the issuance of this Request for Proposals, and ending on the date of the award of the contract, no person, or entity submitting in response to this Request for Proposals, nor any officer, employee, representative, agent, or consultant representing such a person or entity shall contact any person within the School to engage in discussion of the process of selection or award process except for the School designee for questions listed in this Request for Proposals.

APPENDIX C: ENERGY SERVICES CONTRACT

CONTRACT

This Energy Services Contract (“Contract”) is made by and between the Redwood Coast Montessori School (“School”), and _____ (“ESCO”).

School and ESCO hereby agree as follows:

RECITALS

WHEREAS, Government Code sections 4217.10, *et seq.*, authorize the School, as a public agency, to enter into an energy services agreement wherein the ESCO provides conservation services to the School from an energy conservation facility on terms that its governing body determines are in the best interest of the School;

WHEREAS, pursuant to Government Code section 4217.11(d), “conservation services” include electrical, thermal, or other energy savings resulting from conservation measures, which shall be treated as a supply of such energy;

WHEREAS, through this Contract, the School intends to contract for the engineering, system design, fabrication and installation of photovoltaic solar systems that will result in energy savings to the School and which shall be a supply of energy to the School (the “Project”) at the following sites: Redwood Coast Montessori School (the “Project Sites” or “Sites”, and each individually a “Site”), consistent with the terms of Government Code section 4217.10, *et seq.*;

WHEREAS, the School’s Governing Board, after holding a hearing at a regularly scheduled public hearing and after having provided two weeks advanced notice of such hearing, made all findings required by Government Code section 4217.12 for the School to enter into this Contract;

WHEREAS, the ESCO shall engineer, design, and construct the Project pursuant to this Contract, including but not limited to certain General Terms and Conditions and other Contract Documents (as that term is defined in the General Conditions), which Contract Documents are incorporated into the Agreement by this reference;

NOW, THEREFORE, in consideration of the covenants hereinafter contained in this Contract, the School and ESCO agree as follows:

1. Description of Work

The ESCO will provide the design, construction, commissioning, and installation of an ECAA funded project for Redwood Coast Montessori School. The ESCO agrees to furnish all labor, materials, equipment, plant, tools, supervision, appurtenances, and services, including transportation and utilities, required to perform and satisfactorily complete all work required for the Project. The ESCO agrees to furnish any and all electrical and mechanical designs and specifications including but not limited to performance specifications, panel layout and mounting

diagrams, electrical drawings and calculations, mechanical drawings and calculations complete with stamp and signature of a licensed California Engineer.

2. Contract Documents

The Contract Documents consist of the Complete Proposal Documents, as submitted by ESCO, including applicable drawings and calculations, the Contract, any Amendment thereto, Schematic Drawings and Specifications, Supplementary General Conditions, if any, General Conditions, Detailed Project Schedule, Proposal Requirements, Request for Proposals, Disabled Veteran Business Enterprises Requirements (if applicable), Labor Compliance Program (if applicable), all addenda, required bond(s) and insurance certificates, completed Project Questionnaire, ESCO Prequalification, all of which are incorporated herein by this reference. All Contract Documents are intended to coordinate so that any work called for in one document and not mentioned in another document is to be executed as if mentioned in all documents.

3. Proposals & Compensation

As full compensation for ESCO's complete and satisfactory performance of the work and activities described in the Contract Documents, School agrees to pay ESCO, and ESCO agrees to accept the sum of _____ (\$ _____), which shall be paid to the ESCO according to the Contract Documents.

4. Prevailing Wages

This Project is subject to prevailing wage requirements, and ESCO and its Subcontractors are required to pay all workers employed for the performance of this contract no less than the applicable prevailing wage rate for each such worker.

5. Time for Completion

The starting date of the Contract shall be the day listed by the School in the Notice to Proceed and the ESCO shall fully complete all the work as detailed in accordance with Appendix A of the RFP: Proposed Project Schedule. Time is of the essence in the performance of this Contract.

6. Liquidated Damages

Liquidated damages for ESCO's failure to complete the Contract within the time fixed for completion inclusive of milestone dates are established in the amount of \$200 per day per each Milestone until that Milestone is completed.

IN WITNESS WHEREOF, the parties agree to the terms of this Contract on the day and year written below.

School Authorized Signature

ESCO

Resolution No. _____

ESCO License No and Expiration Date

Date

By:

Individual Signature

Title

Date

For:

Corporation or Partnership

If Corporation, Seal Below.

**General Conditions to Design-Build Contract for:
Heat Pumps and Solar Photovoltaic System
Redwood Coast Montessori School**

GENERAL CONDITIONS TABLE OF CONTENTS

1. DEFINITIONS	20
2. PROJECT MANAGER	21
3. CONTRACT DOCUMENTS	21
4. INTENT OF DRAWINGS AND SPECIFICATIONS	22
5. TRADE DIVISIONS	23
6. MASTER MANDATORY PROVISIONS	23
7. ESCO	24
8. RESPONSIBILITY OF ESCO	24
9. SUBCONTRACTORS	25
10. PERFORMANCE AND PAYMENT BONDS	25
11. INSURANCE	26
12. CODES AND REGULATIONS	29
13. PERMITS AND TAXES	29
14. PATENTS AND ROYALTIES	29
15. SAFETY AND FIRE PREVENTION	30
16. HAZARDOUS MATERIALS	30
17. TEMPORARY FACILITIES	31
18. SIGNS	32
19. TIME	32
20. PRE-CONSTRUCTION & CONSTRUCTION SCHEDULE	32
21. DELAYS AND TIME EXTENSIONS	33

22. LIQUIDATED DAMAGES	33
23. SCHOOL'S RIGHT TO STOP WORK; TERMINATION OR SUSPENSION OF THE CONTRACT	34
24. ASSIGNMENT OF CONTRACT	35
25. COORDINATION WITH OTHER CONTRACTS	35
26. SUBMITTALS: SHOP DRAWINGS, CUTS AND SAMPLES	36
27. PAYMENTS	37
28. MODIFICATIONS OF CONTRACT	38
29. INDEMNITY	41
30. WARRANTY OF TITLE	41
31. USE OF COMPLETED PARTS OF THE WORK BEFORE ACCEPTANCE	41
32. GUARANTEE & WARRANTY	41
33. PROTECTION OF WORK AND PROPERTY	42
34. USE OF ROADWAYS AND WALKWAYS	42
35. MATERIALS	43
36. SUBSTITUTIONS	43
37. TESTING	44
38. INSPECTION	44
39. CLEANUP	45
40. CONSTRUCTION WASTE MANAGEMENT	45
41. INSTRUCTIONS AND MANUALS	48
42. AS-BUILT DRAWINGS	48
43. SUBSTITUTION OF SECURITIES	48
44. NO DISCRIMINATION	49
45. LABOR STANDARDS	49
46. GENERAL RATE OF PER DIEM WAGES	50

47. RECORD KEEPING	50
48. PROJECT COMPLETION	51
49. TRENCHING OR OTHER EXCAVATIONS	52
50. RESOLUTION OF CONSTRUCTION CLAIMS	53
51. DISABLED VETERANS PARTICIPATION GOALS (APPLIES TO K-12 SCHOOLS ONLY.)	55
52. RETENTION OF DVBE RECORDS (APPLIES TO K-12 SCHOOLS ONLY.)	55
53. FINGERPRINTING (APPLIES TO K-12 SCHOOLS ONLY.)	55
55. DRUG-FREE WORKPLACE CERTIFICATION	56
56. PROVISIONS REQUIRED BY LAW DEEMED INSERTED	57
57. GENERAL PROVISIONS	57
APPENDIX D: PERFORMANCE BOND	59
APPENDIX E: PAYMENT BOND	61
APPENDIX F: WARRANTY BOND	63
APPENDIX G: SUBCONTRACTOR LIST FORM	65
APPENDIX H: TECHNICAL FACILITY PROFILE	66
APPENDIX I: FLOOR PLAN	67
APPENDIX J: SITE PLAN	68

1. DEFINITIONS

Addendum: A written change or revision to the Contract Documents issued to the prospective proposers prior to the time of receiving proposals.

Alternate: The sum to be added to or deducted from the base proposal if the change in scope of work as described in Alternates as accepted by the School.

Approved: Approved by the School or the School's authorized representative unless otherwise indicated in the Contract Documents.

Architect: The person or firm holding a valid license to practice architecture or engineering which has been designated (if any designated) to provide architectural or engineering design services on this Project. When Architect is referred to within the Contract Documents and no architect or engineer has in fact been designated, then the matter shall be referred to the School Superintendent or its designer.

As Directed: As directed by the School or its Project Manager, unless otherwise indicated in the Contract Documents.

As Selected: As selected by the School or its Project Manager, unless otherwise indicated in the Contract Documents.

Construction Manager: The individual or entity named as such by the School. If no Construction Manager is designated for the project, all references to the Construction Manager in these Contract Documents shall mean the School and/or its designee.

Contract: The legally binding agreement between the School and the ESCO wherein the ESCO agrees to furnish the labor, materials, equipment, and appurtenances required to perform the work described in the Contract Documents and the School agrees to pay the ESCO for such work.

Contract Documents: The Contract Documents are described in the Contract for this Project.

School and/or Owner: The School, its governing board, authorized officers and employees, and authorized representatives.

ESCO: The person or entity holding a valid license in the State of California required for performing this Project and who has contracted with the School to perform the construction work described in the Contract Documents. The term ESCO shall be construed to mean all of the officers, employees, Subcontractors, suppliers, or other persons engaged by the ESCO for the work of this Project.

Final Completion: Final Completion is achieved when the ESCO has fully completed all Contract Document requirements, including, but not limited to, all final punch list items and project closeout, to the School's satisfaction.

Furnish: Purchase and deliver to site of installation.

Governing Board: The Governing Board of the Redwood Coast Montessori School.

Inspector: The person engaged by the School, pursuant to Section 17311 of the Education Code, to inspect the workmanship, materials, and manner of construction of buildings or portions of buildings to determine if such construction complies with the Contract Documents and applicable codes and regulations.

Indicated (or) As Shown: Shown on drawings and/or as specified.

Install: Fix in place, for materials; and fix in place and connect, for equipment.

Modification: An authorized change to the Contract Documents which may or may not include a change in contract price and/or time.

Project: The total construction work and activities described in these Contract Documents.

Project Manager: Redwood Coast Energy Authority (RCEA) serves as the ECAA-Ed Project Manager for this Project.

Proposal: The properly completed and signed proposal to perform the construction work for the Project as described in the Contract Documents.

Secure: Obtain.

Subcontractor: A person, firm, or corporation duly licensed in the State of California who has a contract with the ESCO to furnish labor, materials, and equipment, and/or to install materials and equipment for work in this Contract.

2. PROJECT MANAGER

a. Role and Responsibilities

The Project Manager is responsible for the general oversight of all the working drawings, technical Specifications, sketches, and other information necessary to define the work covered by these Contract Documents as generated by the ESCO. The Project Manager shall visit, inspect, and observe the construction to determine general compliance with the Contract Documents. The Project Manager shall evaluate the shop drawings, samples and other submittals required in the technical Specifications, and maintain an up-to-date log of all such items processed. The Project Manager will consult with the School, ESCO, and any state, county or city agency having jurisdiction over the work whenever necessary to further the best interests of the Project.

b. Disputes

Should any dispute arise respecting interpretation of the drawings and Specifications, the value of any work done or of any work omitted, or of any extra work which ESCO may be required to do or respecting the size of any payment to ESCO during the performance of this Contract, the dispute shall be decided by the Project Manager, and the Project Manager's decision shall be final and conclusive.

3. CONTRACT DOCUMENTS

a. Contents and Precedence

The Contract Documents consist of the executed Contract and all Addenda, all approved change orders, the completed Request for Proposals Form, the required Bonds and the Insurance forms, the Request for Proposals, any Addendums, the Notice of Award, the Notice to Proceed, the General Conditions, any supplemental Conditions, the Technical Specifications, and the Drawings. The Contract Documents are complementary, and anything required by one shall be as binding as if required by all. In case of conflicts within the Contract Documents, the order of precedence of interpretation shall be as listed above, with the executed Contract and any change order thereto having priority, and subsequent Addenda having priority over prior Addenda only to the extent modified by the subsequent Addenda. In case of conflict within the drawings, larger scale drawings shall govern smaller scale drawings, and written dimensions shall govern over scaled dimensions.

b. Ambiguities, Errors, and Inconsistencies

If, in the opinion of the ESCO, the construction details indicated on the drawings or otherwise specified are in conflict with accepted industry standards for quality construction and therefore might interfere with its full guarantee of the work involved, the ESCO shall promptly bring this information to the attention of the Project Manager for appropriate action before submittal of the proposal.

ESCO's failure to request clarification or interpretation of an apparent ambiguity, error or inconsistency waives that ESCO's right to thereafter claim any entitlement to additional compensation based upon an ambiguity, inconsistency, or error, which should have been discovered by a reasonably prudent ESCO, subject to the limitations of Public Contract Code §1104. During the Project, should any discrepancy appear, or any misunderstanding arise as to the import of anything contained in the Contract Documents, the matter shall be promptly referred to the Project Manager, who will issue instructions or corrections.

c. Lines and Planes

All lines and planes appearing on contract drawings to be horizontal or vertical and not explicitly indicated otherwise shall be constructed true and plumb. All lines and planes appearing on contract drawings to intersect at right angles and not explicitly indicated otherwise shall be constructed at true right angles. Where details are indicated covering specific conditions, such details also apply to all similar conditions not specifically indicated.

d. Standards

The specification standards of the various sections of the Specifications shall be the procedural, performance, and material standards of the applicable association publications identified and shall be the required level of installation, materials, workmanship, and performance for the applicable work. Except where a specific date of issue is mentioned hereinafter, references to specification standards shall mean the edition, including amendments and supplements, in effect on the date of the Request for Proposals. Where no standard is identified, and a manufacturer is specified, the manufacturer's specifications are the standards. All standards shall be subordinate to the requirements of the applicable codes and regulations.

e. Reference to the Singular

Wherever in the Specifications an article, device or piece of equipment is referred to in the singular number; such reference shall include as many such items as are shown on Drawings or required to complete the installation.

4. INTENT OF DRAWINGS AND SPECIFICATIONS

a. Drawings and Specifications are to be read as an integrated document. The ESCO shall promptly report to the Project Manager any ambiguities, discrepancies, or errors which come to the ESCO's attention.

b. Figured dimensions shall be followed in preference to scaled dimensions, and the ESCO shall make all additional measurements necessary for the work and shall be responsible for their accuracy. Before ordering any material or doing any work, the ESCO shall verify all measurements at the Project site and shall be responsible for the correctness of same.

c. It is the intent of the drawings and Specifications to show and describe complete installations. Items shown but not specified, or specified but not shown, shall be included unless specifically omitted.

d. The Specifications shall be deemed to include and require everything necessary and reasonably incidental to the completion of all work described and indicated on the drawings, whether particularly mentioned or shown, or not.

5. TRADE DIVISIONS

Segregation of the Specifications into the designated trade divisions is only for the purpose of facilitating descriptions and shall not be considered as limiting the work of any subcontract or trade. Subject to other necessary provisions set forth in the Specifications, the terms and conditions of such limitations or inclusions shall lie solely between the ESCO and its Subcontractors. "Scope" as indicated in each section of the Specifications shall serve only as a general guide to what is included in that section. Neither the stated description nor the division of the plans and Specifications to various sections, which is done solely for convenience, shall be deemed to limit the work required, divide, or indicate it by labor jurisdiction or trade practice, or set up any bidding barriers to the various Subcontractors or suppliers.

a. The ESCO shall be responsible for the proper execution of all work required by the Contract Documents and for allocating such portions as the ESCO sees fit to the various Subcontractors, subject to applicable law. The ESCO is cautioned that the various individual sections may not contain all work that the ESCO may wish to allocate to a particular Subcontractor or everything bearing on the work of a particular trade, some of which may appear in other portions of the plans or Specifications.

b. If the ESCO elects to enter into any subcontract for any section of the work the ESCO assumes all responsibility for ascertaining that the Subcontractor for the work is competent, licensed, solvent, thoroughly acquainted with all conditions and legal requirements of the work, has included all materials and appurtenances in connection therewith in the subcontract, and has performed its work in strict compliance with the Contract Documents.

c. It shall be the responsibility of the ESCO to notify each prospective Subcontractor at the time of request for proposals of all portions of the Contract Documents, including the General Conditions, Supplementary Conditions, and any parts of sections of Specifications or plans that the ESCO intends to include as part of the subcontract.

6. MASTER MANDATORY PROVISIONS

a. Any material, item, or piece of equipment mentioned, listed, or indicated without definition of quality, shall be consistent with the quality of adjacent or related materials, items, or pieces of equipment on the Project and in accordance with best practices.

b. Any method of installation, finish, or workmanship of an operation called for, without definition of standard of workmanship, shall be followed or performed and finished in accordance with best practices and consistent with adjacent or related installations on the Project.

c. Any necessary material, item, piece of equipment or operation not called for but reasonably implied as necessary for proper completion of the work shall be furnished, installed, or performed and finished; and shall be consistent with adjacent or related materials, items, or pieces of equipment on the Project, and in accordance with best practices.

d. Names or numbered products are to be used according to the manufacturers' directions or recommendations unless otherwise specified.

7. ESCO

a. The ESCO shall perform all the work and activities required by the Contract Documents and furnish all labor, materials, equipment, tools, and appurtenances necessary to perform the work and complete it to the School's satisfaction within the time specified. The ESCO shall at all times perform the work of this Contract in a competent and efficient manner and, if not specifically stated, accomplish the work according to the best standards of construction practice. The ESCO in no way is relieved of any responsibility by the activities of the Project Manager, engineer, or inspector in the performance of such duties.

b. The ESCO shall employ a full-time competent superintendent and necessary assistants who shall have complete authority to act for the ESCO on all matters pertaining to the work. The superintendent shall be satisfactory to the School and, if not satisfactory, shall be replaced by the ESCO with one that is acceptable. Also, the superintendent shall not be changed without the written consent of the School unless the superintendent ceases to be employed by the ESCO.

c. ESCO shall make the layout of lines and elevations and shall be responsible for the accuracy of both the ESCO's and the Sub-contractors' work resulting there from. All dimensions affecting proper fabrication and installation of all Contract work must be verified by the ESCO prior to fabrication and installation by taking field measurements of the true conditions. The ESCO shall take, and assist Subcontractors in taking, all field dimensions required in performance of the work, and shall verify all dimensions and conditions on the site. If there are any discrepancies between dimensions in drawings and existing conditions which will affect the work, the ESCO shall promptly bring such discrepancies to the attention of the Project Manager for adjustment before proceeding with the work. ESCO shall be responsible for the proper fitting of all work and for the coordination of all trades, Subcontractors and persons engaged upon this Contract.

d. ESCO shall do all cutting, fitting, or patching of ESCO's work that may be required to make its several parts come together properly and fit it to receive or be received by work of other ESCOs as shown, or reasonably implied by, the drawings and Specifications for the completed work. Any cost incurred by the School due to defective or ill-timed work shall be borne by the ESCO.

8. RESPONSIBILITY OF ESCO

a. ESCO shall be held strictly responsible for the proper performance of all work covered by the Contract Documents, including all work performed by Subcontractors. All work performed under this Contract shall comply in every respect to the rules and regulations of all agencies having jurisdiction over the Project or any part thereof.

b. ESCO shall perform the duties and submit Verified Reports if required as defined in Sections 4-336 and 4-343 (c), Group 1, Chapter 4, Part I, Title 24, California Code of Regulations ("CCR"). The duties of the ESCO are as defined in Section 4-343, Group 1, Chapter 4, Part I, Title 24, of the CCR. ESCO may want to keep and make available a copy of Title 24 of the CCR at the job site at all times.

c. Where, because of short supply, any item of fabricated materials and/or equipment, indicated on drawings or specified, is unobtainable and it becomes necessary, with the consent of the Project Manager, to substitute equivalent items differing in details or design, the ESCO shall promptly submit complete drawings and details indicating the necessary modifications of the work. This

provision shall be governed by the terms of the General Conditions regarding Submittals: Shop Drawings, Cuts and Samples.

d. With respect to work performed at and near a school site, ESCO shall at all times take all appropriate measures to ensure the security and safety of students and staff, including, but not limited to, ensuring that all of ESCO's employees, Subcontractors, and suppliers entering school property strictly adhere to all applicable School policies and procedures, e.g., sign-in requirements, visitor badges, and access limitations.

9. SUBCONTRACTORS

a. Nothing contained in the Contract Documents shall create any contractual relationship between any Subcontractor and the School. The School shall be deemed to be the third-party beneficiary of the contract between the ESCO and each Subcontractor. If the ESCO does not specify a Subcontractor for any portion of the work to be performed under this Contract, as required by law, ESCO shall perform that portion of the work with its own forces. The ESCO shall not substitute any other person or firm as a Subcontractor for those listed in the proposal submitted by the ESCO, without the written approval of the School and in conformance with the requirements of the Public Contract Code. The School reserves the right of approval of all Subcontractors proposed for use on this Project, and to this end, may require financial, performance, and such additional information as is needed to secure this approval. If a Subcontractor is not approved, the ESCO shall promptly submit another firm of the same trade for approval.

b. The ESCO shall insert appropriate provisions in all subcontracts pertaining to work on this Project requiring the Subcontractors to be bound by all applicable terms of the Contract Documents. The ESCO shall be as fully responsible for the acts and omissions of the Subcontractors, and of persons either directly or indirectly employed by them, as the ESCO is for the acts and omissions of persons directly employed by the ESCO.

c. The ESCO shall provide a Subcontractor List Form, in the form of **Appendix G** attached hereto, for any subcontractor performing more than one half of one percent of work on the project.

10. PERFORMANCE AND PAYMENT BONDS

a. As directed in the Notice of Award, the ESCO shall file with the School the following bonds, using the bond forms provided with these Contract Documents:

1) A corporate surety bond, in a sum not less than 100 percent of the amount of the Contract, to guarantee the faithful performance of the Contract, substantially in form of **Appendix D**, attached hereto.

2) A corporate surety bond, in a sum not less than 100 percent of the amount of the Contract, to guarantee the payment of wages for services engaged and of bills contracted for materials, supplies, and equipment used in the performance of the Contract, substantially in the form of **Appendix E**, attached hereto.

b. Corporate sureties on these bonds and on bonds accompanying proposals must be admitted sureties as defined by law, legally authorized to engage in the business of furnishing surety bonds in the State of California. All sureties and bond forms must be satisfactory to the School. Failure to submit the required bonds within the time specified by the Notice of Award, using the forms provided by the School, may result in cancellation of the award of Contract.

- c. The amount of the Contract, as used to determine the amounts of the bonds, shall be the total amount fixed in the ESCO's proposal for the performance of the required work.
- d. During the period covered by the Contract, if any of the sureties upon the bonds shall become insolvent or unable, in the opinion of the School, to pay promptly the amount of such bonds to the extent to which surety might be liable, the ESCO, within thirty (30) days after notice given by the School to the ESCO, shall provide supplemental bonds or otherwise substitute another and sufficient surety approved by the School in place of the surety becoming insolvent or unable to pay. If the ESCO fails within such thirty (30) day period to substitute another and sufficient surety, the ESCO shall, if the School so elects, be deemed to be in default in the performance of its obligations hereunder, and the School, in addition to any and all other remedies, may terminate the Contract or bring any proper suit or other proceedings against the ESCO and the sureties or any of them, or may deduct from any monies then due or which thereafter may become due to the ESCO under the Contract, the amount for which the surety, insolvent or unable to pay, shall have been liable on the bonds, and the monies so deducted shall be held by the School as collateral security for the performance of the conditions of the bonds.
- e. Provide one electronic copy and two hardcopy sets of the bonds to the Project Manager to send to the School for wet signatures.

11. INSURANCE

- a. ESCO shall obtain the following insurance from a company or companies acceptable to the School. All required insurance must be written by a company licensed to do business in the State of California at the time the policy is issued. All required insurance shall be equal to or exceed an A VIII rating as listed in Best's Insurance Guides' latest edition. On a case-by-case basis, the School may accept insurance written by a company listed on the State of California Department of Insurance List of Eligible Surplus Lines ("LESLI List") with a rating of A VIII or above as listed in Best's Insurance Guides' latest edition. Required documentation of such insurance shall be furnished to the School within the time stated in the Notice of Award. ESCO shall not commence work, nor shall it allow its employees or Subcontractors or anyone to commence work until all insurance required hereunder has been submitted and approved in writing by the School and a notice to proceed has been issued.
- b. ESCO shall take out and maintain at all times during the life of this Contract, up to the date of acceptance of the work by the School, the following policies of insurance:
- 1). General Liability Insurance: Personal injury and replacement value property damage insurance for all activities of the ESCO and its Subcontractors arising out of or in connection with this Contract, written on a comprehensive general liability form including ESCO's protected coverage, blanket contractual, completed operations, vehicle coverage and employer's non-ownership liability coverage, in an amount no less than either
 - a. \$1,000,000.00 combined single limit personal injury and property damage for each occurrence and \$2,000,000.00 annual aggregate with a \$0 umbrella/excess; or
 - b. \$2,000,000.00 annual combined single limit
 - 2). Builders' Risk Insurance: For a proposal over \$225,000, ESCO shall procure and maintain builders' risk insurance (all-risk coverage) for an amount equal to one hundred percent of the Contract sum for the benefit of the School, and the ESCO and Subcontractors as their interest may appear. In projects involving no structural change or building construction, this requirement may be waived in writing, at the School's sole option.

These policies shall include the following coverage:

- 1). The inclusion of more than one insured shall not operate to impair the rights of one insured against another insured and the coverages afforded shall apply as though separate policies have been issued to each insured.
- 2). This policy does not exclude explosion, collapse, underground excavation hazard, or removal of lateral support.

c. Endorsements:

- 1). The certificate(s) for both the General Liability Policy and the Automobile Liability Policy, as well the Builders' Risk Policy if required above, **shall be endorsed with the following specific language:**

“The Redwood Coast Montessori School is named as an additional insured for all liability arising out of the operations by or on behalf of the named insured, and this policy protects the additional insured, its officers, agents, and employees against liability for bodily injuries, death or property damage or destruction arising in any respect directly or indirectly in the performance of the Contract.”

- 2) The certificates must state that the insurance is under an occurrence based, and not a claims-made policy (policies). Both the General Liability Policy and the Builders' Risk Policy specified above shall be endorsed with the following specific language:

- a. The insurance provided herein is primary and no insurance held or owned by the School shall be called upon to contribute to a loss.
- b. Coverage provided by this policy shall not be reduced or canceled without thirty (30) days written notice given to the School by certified mail.

d. Professional Liability Insurance for Engineer of Record (Errors and Omissions):

If applicable, ESCO shall maintain in force for the period covered by this Agreement, professional liability (errors and omissions) insurance covering the Engineer of Record's activities, in the amount not less than \$2,000,000 with an insurance carrier satisfactory to School. In addition, to the extent that the activities and services of engineers or consultants retained by ESCO are not covered under ESCO's professional liability insurance, ESCO shall require each engineer and consultant to obtain and maintain a policy of professional liability insurance in an amount of not less than \$2,000,000 with an insurance carrier satisfactory to School, before commencing services on the Project. ESCO shall provide a copy of the insurance policies to the School upon request.

e. Automobile Liability Insurance:

ESCO shall maintain in force for the period covered by this Agreement, automobile liability insurance covering bodily injury and property damage in an amount no less than \$1,000,000 combined single limit for each occurrence; \$2,000,000 aggregate. Said insurance shall include coverage for owned, hired, rented, and non-owned vehicles. All certificates must state that the insurance is under an occurrence based, and not a claims-made policy (policies).

f. Documentation:

Within ten (10) calendar days following issuance of the Notice of Award of the Contract, the following documentation of insurance shall be submitted to the Project Manager electronically to send to the School for approval prior to issuance of the Notice to Proceed, signed certificates of insurance showing the limits of insurance provided and copies of the specified endorsements for each policy. Certified copies of all policies shall be provided to the School upon request.

g. If the ESCO fails to maintain such insurance, the School may take out such insurance to cover any damages for which the School might be held liable on account of the ESCO's failure to pay such damages and deduct and retain the amount of the premiums from any sums due the ESCO under the Contract.

h. Workers' Compensation Insurance:

1). Within ten (10) calendar days following issuance of the Notice of Award of the Contract, the ESCO shall submit to Project Manager electronically in order to send to the School satisfactory proof that the ESCO **and all Subcontractors it intends to employ** have procured, for the period covered by the Contract, full Workers' Compensation insurance and employer's liability with limits of at least \$1,000,000 with an insurance carrier satisfactory to the School for all persons whom the ESCO may employ in carrying out the work contemplated under this Contract in accordance with the Workers' Compensation Insurance and Safety Act, approved May 26, 1913, and all acts amendatory or supplemental thereto (the "Act"). Such insurance shall be maintained in full force and effect during the period covered by the Contract. In the event the ESCO is self-insured, ESCO shall furnish a Certificate of Permission to Self-Insure, signed by the Department of Industrial Relations Administration of Self-Insurance, Sacramento, California.

2). If the ESCO fails to maintain such insurance, the School may take out worker's compensation insurance to cover any compensation which the School might be liable to pay under the provisions of the Act, by reason of any employee of the ESCO being injured or killed and deduct and retain the amount of the premiums for such insurance from any sums due the ESCO under the Contract, or otherwise recover that amount from the ESCO or the Surety.

3). If an injury occurs to any employee of the ESCO for which the employee, or the employee's dependents in the event of the employee's death, is entitled to compensation under the provisions of the Act, or for which compensation is claimed from the School, the School may retain from the sums due the ESCO under this Contract an amount sufficient to cover such compensation, as fixed by the Act, until such compensation is paid, or until it is determined that no compensation is due, and if the School is compelled to pay such compensation, it will deduct and retain from such sums the amount so paid, or otherwise recover this sum from the ESCO or its Surety.

4). The policies represented by the certificates shall be endorsed with a Waiver of Subrogation and must contain the provision (and the certificates must so state) that the insurance cannot be canceled until thirty (30) days after written notice of intended cancellation has been given to the School.

12. CODES AND REGULATIONS

- a. The ESCO shall be knowledgeable regarding and shall comply with applicable portions of California Code of Regulations Title 24, the applicable Building Code, and all other codes, ordinances, regulations, or orders of properly constituted authority having jurisdiction over the work of this Project. The ESCO shall examine the Contract Documents for compliance with these codes and regulations and shall promptly notify the Project Manager of any discrepancies.
- b. All work, and materials shall be in full accordance with the latest rules and regulations of the Safety Orders of the Division of Industrial Safety, the National Electric Code, the Uniform Plumbing Code published by the Western Plumbing Officials Association, and other applicable State laws or regulations. Nothing in the Project plans or Specifications is to be construed to permit work not conforming to the applicable Codes. Buildings and/or all other construction covered by this Contract shall meet all the regulations for access by the physically handicapped as administered by the Division of the State Architect, and as may be required by federal or state law.
- c. If the work under this Contract is for the construction of a school building as defined by the Education Code, then the following provisions shall apply to the Contract:
 - 1). All work shall be executed in accordance with the current requirements of Sections 17280 et seq. or Sections 81130 of the Education Code and California Code of Regulations: Title 24 and Title 19. No deviations from the approved plans and Specifications will be permitted except upon a Change Order or Addenda, signed by the School and Architect and approved by the appropriate local building division and the State Fire Marshal, if applicable.
 - 2). Prior to the start of construction, School shall employ a Project Inspector to provide inspection services as defined in Title 24, California Code of Regulations and pursuant to Section 17311 of the Education Code. The Owner shall pay for the costs of the project inspection services, except as indicated in the General Conditions, Article 38 and the plans and Specifications. A copy of current California Code of Regulations Title 24, approved sets of Plans and Specifications, addenda and change orders, may be kept by the School Job Inspector on the job at all times during construction.

13. PERMITS AND TAXES

- a. The ESCO shall obtain and pay for all permits, fees and licenses that are required in order to perform the work under this Contract. The School shall pay connection charges and meter costs for new permanent utilities required by these Contract Documents. The ESCO shall notify the School sufficiently in advance to submit requests for service to the appropriate utility companies to insure connections or installation of utility services in accordance with the Project schedule.
- b. The ESCO shall pay for all taxes on materials and equipment. The School is exempt from Federal Excise Tax. ESCO shall not pay Federal Excise Tax on any item in this Contract.

14. PATENTS AND ROYALTIES

All fees or claims for patents, royalties or licenses on materials, equipment or processes used in the performance of work on this Project shall be included in the amount of the proposal. The ESCO shall indemnify, defend, and hold harmless the School, its Governing Board, the Project Manager, and their officers and employees, from all claims or liability, including costs and expenses, which may arise from the use on this Project of any patented or copyrighted materials, equipment, or processes.

15. SAFETY AND FIRE PREVENTION

- a. The ESCO, Subcontractors and all of their agents and employees shall fully comply with all of the provisions and requirements of CAL/OSHA, Title 8, California Code of Regulations, and all other safety codes applicable to the Project. The ESCO shall always take thorough precautions for the protection of persons and property and shall be liable for all damages to persons or property, either on or off the site, which occur as a result of ESCO's prosecution of the work. The ESCO shall obtain permits for, install, and maintain in safe condition barricades, walkways, fences, railings, and whatever other safeguards that may be necessary to protect persons and property from damage as a result of the construction under this Contract.
- b. ESCO is required to ensure Material Safety Data Sheets ("MSDS") are available in a readily accessible place at the work site for any material requiring a MSDS pursuant to the federal "Hazard Communication" standard or employee "right to know" laws. ESCO is also required to ensure proper labeling on materials brought on the job site such that any person working with the material or within the general area of the material is informed of the hazards of the material and follows proper handling and protection procedures. A copy of the MSDS shall also be promptly submitted directly to the School.
- c. ESCO shall not endanger any work by cutting, excavating, or otherwise altering the work and shall not cut or alter the work of any other ESCO except with the written consent of the Project Manager, nor overload any new or existing structures by the placing or storage of materials, equipment, or other items thereon, and, if necessary, shall provide calculations proving the safety in so doing.
- d. If it is necessary to work at night, or where daylight is obscured, the ESCO shall provide and maintain lighting of an adequate level to properly prosecute the work, to permit the thorough inspection of same, and to ensure the safety to workers and others.
- e. ESCO shall take extraordinary care to prevent fires and keep all flammable materials and oily rags in tightly closed metal containers. ESCO shall exercise particular care when welding or cutting, and with regard to the disposition of waste materials, the nature and quantity of which might create or increase a fire hazard.

16. HAZARDOUS MATERIALS

Unless otherwise specified, this Contract does not include the removal, handling, or disturbance of any hazardous substances or materials encountered in the new construction or on the Project grounds. If such substances or materials are encountered, work shall cease in that area and the School shall be promptly notified to take appropriate action for removal or otherwise abating the condition in accordance with current regulations applicable to the School.

- a. General
 - 1). No asbestos, asbestos-containing products or other hazardous materials shall be used in this construction or in any tools, devices, clothing, or equipment used to further this construction.
 - 2). Asbestos and/or asbestos containing products shall be defined as all items containing but not limited to chrysotile, crocidolite, amosite, anthophyllite, tremo-lite or actinolite.
 - 3). Any or all material containing greater than one tenth of one percent (>.1%) asbestos shall be defined as asbestos-containing material.

4). Any disputes involving the question of whether material contains asbestos shall be settled by electron microscopy; the cost of any such tests shall be paid by the ESCO.

5). All work or materials found to contain asbestos, or work or material installed with asbestos containing equipment will be immediately rejected and this work shall be removed by the ESCO at no additional cost to the School.

b. Decontamination and Removal of hazardous material from prior work

1). Decontamination and removal of work found to contain asbestos, or work installed with asbestos containing equipment shall be done only under the supervision of a qualified consultant, knowledgeable in the field of asbestos abatement and accredited by the Environmental Protection Agency ("EPA").

2). The asbestos removal ESCO shall be an EPA-accredited ESCO qualified in the removal of asbestos subject to approval of the School.

3) The asbestos consultant shall be chosen and approved by the School which shall have sole discretion and final determination in this matter.

4). The work will not be accepted until asbestos contamination is reduced to levels deemed acceptable by the asbestos consultant.

c. Hold Harmless

1). Interface of work under this contract with work containing asbestos shall be executed by the ESCO at ESCO's risk and at ESCO's discretion with full knowledge of the currently accepted standards, hazards, risks, and liabilities associated with asbestos work and asbestos containing products. By execution of this contract the ESCO acknowledges the above and agrees to hold harmless, as set forth in the indemnity provisions of this Contract, the Owner, its employees, agents and assigns for all asbestos liability which may be associated with this work and agrees to instruct ESCO's employees and agents with respect to the above-mentioned standards, hazards, risks, and liabilities.

2). The ESCO shall, prior to commencement of this work, provide a duly signed and notarized affidavit that ESCO has instructed ESCO's employees and agents with respect to the above-mentioned standards, hazards, risks and liabilities and the contents and requirements of this portion of the Contract Documents.

d. Certification

The ESCO agrees that materials containing asbestos or other hazardous materials as defined in Federal and State law shall not be used in construction.

17. TEMPORARY FACILITIES

a. The ESCO shall obtain permits for, install, and maintain in safe condition all scaffolds, hoisting equipment, barricades, walkways, or other temporary structures that may be required to accomplish the work. Such structures shall be adequate for the intended use and capable of safely accepting all loads that may be imposed upon them. They shall be installed and maintained in accordance with all applicable codes and regulations.

b. The ESCO shall provide and maintain temporary heat from an approved source whenever in the course of the work it may become necessary for curing, drying or warming spaces as may be required for the proper installation of materials or finishes. The ESCO shall provide and maintain any and all facilities that may be required for dewatering in order that work may proceed on the

project. If it is necessary for dewatering to occur continually, the ESCO shall have on hand whatever spare parts or equipment that may be required to avoid interruption of service or work.

c. The ESCO shall promptly remove all such temporary facilities when they are no longer needed for the work or on completion of the project. The ESCO shall repair any damage to premises or property which resulted from the construction, use, or removal of temporary facilities and shall restore the premises and property to their original condition.

d. See the Supplemental General Conditions and/or specifications for requirements concerning temporary sanitary facilities and utilities.

18. SIGNS

No signs may be displayed on or about the School's property (except those which may be required by law) without the School's prior written approval of size, content, and location. Any signs required by the School will be designated in the Supplemental General Conditions.

19. TIME

a. The ESCO shall commence the work on the date indicated in the Notice to Proceed. Time is of the essence regarding the Contract work, and the ESCO shall prosecute the work diligently and regularly at such a rate of progress as to ensure completion of this Project within, or sooner than, the time specified.

b. The ESCOs and Subcontractors shall investigate and become aware of the amount of time required for the delivery of all equipment and materials required to perform the work under this Contract, and no extension of time shall be granted due to failure to order the equipment and materials sufficiently before their incorporation into the work so as to avoid delay to the Project.

c. The ESCO and Subcontractors shall provide and maintain enough workforce, materials, and equipment to ensure a rate of construction progress that will complete the Project within or sooner than the time specified and according to the schedule of work. If, in the School's opinion, the ESCO and/or Subcontractors are not prosecuting the work at a sufficient rate of progress to meet the Project schedule, the School may direct the ESCO to provide additional workforce, materials or equipment, or to work additional hours, holidays or weekends without additional cost to the School until the work is progressing in a manner satisfactory to the School. Failure to prosecute the work in a timely manner according to the Project schedule is considered a breach of Contract and shall be cause for termination of the Contract.

20. PRE-CONSTRUCTION & CONSTRUCTION SCHEDULE

a. Within fifteen (15) calendar days after the Notice of Award of Contract, the ESCO shall prepare and submit to the Project Manager and School an electronic version of the as planned construction schedule showing in detail how the ESCO plans to prosecute the work within the time set for Final Completion. The schedule shall include the work of all trades necessary for construction of the Project and shall be sufficiently complete and comprehensive to enable progress to be monitored on a day-by-day basis. The information for each activity shall include at a minimum the activity description, duration, start date and completion date.

b. The ESCO shall take care in the preparation of the schedule to ensure that it represents an accurate and efficient plan for accomplishing the work. If the Project is more than one week behind schedule, it must be promptly revised showing how the ESCO plans to complete the work, but in no case shall it show a completion date later than that required by the Contract, unless a time extension has been granted. The current schedule shall be kept posted in the ESCO's project office on site.

c. The ESCO shall be responsible for the coordination of all work necessary and pertaining to the construction whether actually a part of this Contract or attendant thereto. The ESCO shall notify the School and various utility companies, as far as possible in advance of their required work, in order that work schedules may be developed for all concerned, which will permit the most effective and timely accomplishment of the entire project.

21. DELAYS AND TIME EXTENSIONS

a. The ESCO may be granted a time extension if the ESCO encounters an unavoidable delay of the work due to causes completely beyond the ESCO's control and which the ESCO could not have avoided by the exercise of reasonable care, prudence, foresight, and diligence. Causes for which a claim for extension of time may be made include acts of the public enemy, acts of another ESCO in the performance of another contract with the School, priority of a governmental agency for materials or equipment, fire, flood, violent windstorm, epidemic, quarantine restriction, strike, freight embargo, or weather of an unusually severe nature. The ESCO will not be granted time extensions for weather conditions which are normal for the location of the Project, according to the U. S. Weather Bureau Records.

b. A request for extension of time and compensation related thereto shall be made in writing to the Project Manager and School within ten (10) calendar days of the date the delay is encountered or shall be deemed waived. The request shall include a detailed description of the reasons for the delay and corrective measures by the ESCO. The request shall be accompanied by evidence that the insurance policies required by the Contract shall be in effect during the requested additional period of time. In order for the Project Manager to consider a request for time extension, the ESCO must prove that the reasons stated for the delay actually caused a delay in portions of the work which will result in completion beyond the date specified in the Contract. The ESCO may also be granted a time extension for a significant change in the scope of work which request for extension of time shall be included in a Contract modification proposal.

c. No damages or compensation or any kind shall be paid to an ESCO because of delays in the progress of work, whether such delays be avoidable or unavoidable, that are not the responsibility of School. School's liability to ESCO for delays for which School is responsible shall be limited to an extension of time unless such delays were unreasonable under the circumstances involved and were not within the contemplation of the parties when the Contract was awarded. The ESCO shall provide to the School the actual, substantiated costs to ESCO for which the ESCO may claim damages from School. Such costs, if any, shall be directly related to the Project, and shall not include costs that would be borne by the ESCO in the regular course of business, including, but not limited to, office overhead and ongoing insurance costs. Delay damages shall not include ESCO or Subcontractor markup for overhead and profit, but only actual, documented, and direct actual costs. The School shall not be liable for any damages which the ESCO could have avoided by any reasonable means including, but not limited to, the more judicious handling of forces or equipment.

d. The granting of an extension of time because of unavoidable delays shall in no way operate as a waiver on the part of the School of the right to collect liquidated damages for other delays or of any other rights to which the School is entitled.

22. LIQUIDATED DAMAGES

a. Should the ESCO fail to achieve Final Completion of this Contract within the time fixed for Final Completion, together with extensions granted by the School for unavoidable delays, ESCO shall become liable to the School in the amount specified in the Contract per calendar day for each

day the Contract remains incomplete beyond the time for Final Completion, as liquidated damages and not as a penalty. ESCO may also be assessed liquidated damages for failure to meet milestones specified in the Contract Documents, regardless of impact on overall Project completion. ESCO shall not be charged with liquidated damages when the delay in completion of the work beyond the time for Final Completion is due to acts of the School. It is expressly stipulated and agreed by ESCO and School that it would be impractical and extremely difficult to fix the actual amount of damages.

b. In addition to any liquidated damages which may be assessed, if ESCO fails to achieve Final Completion of this Contract within the time fixed for Final Completion, together with extensions granted by the School for unavoidable delays, and if as a result School finds it necessary to incur any costs and/or expenses, or if School receives any claims by other contractors, subcontractors, or third parties claiming time or other compensation by reason of ESCO's failure to complete work on time, ESCO shall pay all those costs and expenses incurred by School. These costs and expenses may include but are not limited to such items as rental payments, inspection fees, and additional architectural fees, whether related to the acquisition of facilities or caused by the delay in completion.

c. Any money due or to become due the ESCO may be retained to cover liquidated damages. Should such money not be sufficient to cover the liquidated damages, the School shall have the right to recover the balance from the ESCO or ESCO's sureties.

d. Should the School authorize suspension of the work for any cause, the time work is suspended will be added to the time for completion. Suspension of the work by the School shall not be a waiver of the right to claim liquidated damages as set forth in this section.

e. The assessment of Liquidated Damages does not otherwise limit the right of the Owner to claim a loss or damages incurred by the Owner for reasons other than delay (e.g., damages due to defective work).

23. SCHOOL'S RIGHT TO STOP WORK; TERMINATION OR SUSPENSION OF THE CONTRACT

a. School's Right to Stop Work:

In addition to or as an alternative to any and all other remedies available to the School, if the ESCO fails to correct work which is not performed in accordance with the Contract Documents, or if the ESCO persistently fails to perform the work in accordance with the Contract Documents, the School may by written order direct the ESCO to stop the work, or any portion thereof, until the cause for such order has been eliminated to the satisfaction of the School. However, the right of the School to stop the work shall not give rise to a duty on the part of the School to exercise this right for the benefit of the ESCO or any other person or entity, and the failure of the School to do so shall not be raised as a defense to the ESCO's failure to perform the work in accordance with the Contract Documents.

b. Termination for Cause:

1). If the ESCO refuses or fails to furnish sufficient materials, work force, equipment, and appurtenances to properly prosecute the work in a timely manner, or if ESCO refuses or fails to comply with any provisions of the Contract Documents, or if ESCO should file a bankruptcy petition or make a general assignment for the benefit of ESCO's creditors or if a receiver should be appointed on account of ESCO's insolvency, then the School may give the ESCO and ESCO's Surety written notice of intention to terminate the Contract. Unless within seven (7) calendar days after the serving of such notice upon the ESCO and ESCO's Surety such violation shall cease and arrangements for correction of such conditions shall be made satisfactory to the School,

the Contract shall cease and terminate. In the event of such termination, the School shall immediately serve written notice thereof upon the ESCO and ESCO's Surety.

2). In the event of termination for cause, in addition to all remedies available to the School, the ESCO's Surety shall have the right to take over and perform the Contract; provided, however, that if the Surety does not commence performance within five (5) calendar days from the date of the issuance of such notice of termination, the School may take over the work and prosecute the same to completion by letting another Contract, or by any other method that the School deems advisable. The ESCO and ESCO's Surety shall be liable for any excess cost incurred by the School thereby, and in any such event the School may take possession of such materials, equipment, and other property belonging to the ESCO as may be on the site and use same in completing the work.

c. Termination or Suspension for Convenience:

The School reserves the right, in its sole discretion, to terminate or suspend all or part of the Contract for convenience following three (3) days written notice to the ESCO. In the event of termination or suspension for convenience, ESCO shall have no claims against the School, except:

- 1). The actual cost of labor, materials and services provided pursuant to the Contract, and which have not yet been paid for, as documented by timesheets, invoices, receipts, and the like; and
- 2). Five percent (5%) of the total cost of the work performed as of the date of notice of termination or suspension or five percent (5%) of the value of the work yet to be completed, whichever is less. The parties agree that this amount shall constitute full and fair compensation for all ESCO's lost profits and other damages resulting from the termination or suspension for convenience.

24. ASSIGNMENT OF CONTRACT

The ESCO may not assign or delegate all or any portion of this Contract without the written consent of the School and no such consent shall be given which would relieve the ESCO or its Surety of their responsibilities under the Contract. The ESCO may assign, without liability to the School, monies due the ESCO under the Contract to banks, trust companies or other financial institutions provided written notice thereof is promptly delivered to the School. Assignment of monies earned by the ESCO shall be subject to the same retention as other payments made to ESCO and shall also be subject to setoffs and back charges as provided by this Contract.

25. COORDINATION WITH OTHER CONTRACTS

a. The School reserves the right to do other work or award other contracts in connection with this Project. By entering into this Contract, ESCO acknowledges that there may be other ESCOs on or adjacent to the Project site whose work must be coordinated with that of its own. ESCO expressly warrants and agrees that it will cooperate with other ESCOs and will do nothing to delay, hinder, or interfere with the work of other ESCOs, or that of the School, its Project Manager and Construction Manager. ESCO also expressly agrees that in the event its work is hindered, delayed, interfered with, or otherwise affected by a separate ESCO, its sole remedy will be a direct action against the separate ESCO. To the extent allowed by law, the ESCO expressly waives any remedy against the School, its Project Manager and Construction Manager on account of delay, hindrance, interference, or other such events caused by a separate ESCO.

b. If any part of ESCO's work depends upon the work of a separate ESCO, ESCO shall inspect such other work and promptly report in writing to the School and Project Manager any defects in such other work that render it unsuitable to receive the work of ESCO. Failure of the ESCO to so inspect and report shall constitute an acceptance of the other ESCO's work, except as to defects which the ESCO could not have detected through the reasonable inspection of the other ESCO's work prior to the execution of ESCO's work.

c. If ESCO is aware of a current or potential conflict between ESCO's work and the work of another ESCO on the site and is unable to informally resolve the conflict directly with the other ESCO, ESCO shall promptly provide written notice to the School, with a copy to the Project Manager and the other ESCO, specifying the nature of the conflict, the date upon which the conflict arose, and the steps taken to attempt to resolve the conflict. The School may issue written instructions to address the conflict.

d. If, through ESCO's negligence, any other ESCO or Subcontractor shall suffer loss or damage to the work, ESCO shall make a reasonable effort to settle with such other ESCO and Subcontractor by agreement or arbitration. If such other ESCO or Subcontractor shall assert any claim against the School or Project Manager, on account of any damage alleged to have been so sustained, the School or Project Manager shall notify the ESCO, who shall defend such proceedings at ESCO's own expense and save harmless and indemnify the School and the Project Manager from any such claim.

26. SUBMITTALS: SHOP DRAWINGS, CUTS AND SAMPLES

a. Within fifteen (15) calendar days after the award of the Contract, the ESCO shall prepare and submit to the Project Manager and School an electronic copy of shop drawings, brochures and cut sheets and samples in quantities specified by the Project Manager shall be submitted to the Project Manager for all items for which they are required by the plans and specifications. Prior to transmittal, the ESCO shall examine all submittals for accuracy and completeness in order to verify their suitability for the work and compliance with the Contract Documents and shall sign and date each submittal. Submittals shall be sent for review sufficiently before the items are required for the work so as to cause no delay and shall be in accordance with the project construction schedule.

b. In addition to information furnished as common practice, submittals shall contain the Project name and location, ESCO's name and address, Subcontractor's or supplier's name and address, date of submittal and any revisions, and reference to appropriate specification section, and/or drawing and detail numbers. The ESCO and/or the Subcontractors shall verify in the field all dimensions and relationships to adjacent work necessary to ensure the proper fit of the items submitted. If necessary, the ESCO shall make any corrections required and resubmit with all due haste in the same number as initially required.

c. Review of submittals, shop drawings, cuts or samples by the School or Project Manager shall not relieve the ESCO from complying with the requirements of the Contract Documents.

d. Any materials or equipment installed without approval shall be at the ESCO's own risk, and ESCO may be required to remove any such materials or equipment and install the specified items at ESCO's own cost, including repairs to adjacent work.

27. PAYMENTS

a. Cost Breakdown:

Within 15 calendar days after receipt of the Notice to Proceed, the ESCO shall prepare and submit to the Project Manager and School a cost breakdown (schedule of values) showing the major work items for each trade or operation required in construction of the Project. The work items shall be sufficiently detailed to enable the Project Manager to accurately evaluate the completion percentages requested by the ESCO. The cost for each work item shall include overhead and profit. The total of all work item costs shall equal the amount of the Contract.

b. Scope of Payment:

Payment to the ESCO at the unit price or other price fixed in the Contract for performing the work required under any item or at the lump sum price fixed in the Contract for performing all the work required under the Contract, shall be full compensation for furnishing all labor, materials, equipment and tools necessary to the work, and for performing and completing, in accordance with the Specifications, all work required under the item or under the Contract, and for all expense incurred by the ESCO for any purpose in connection with the performance and completion of the work.

c. Progress Payments:

The ESCO will, on or about the 25th day of each month, make an estimate of the value of the work completed by ESCO in the performance of the Contract. These estimates shall be subject to the review and approval of the Project Manager. The first such estimate will be of the value of the work completed after the ESCO commenced the performance of the Contract, and every subsequent estimate, except the final estimate, will be of the value of the work completed since the immediately preceding estimate. Such estimates will be based on labor, materials and equipment incorporated into the work, and items of materials and equipment delivered to the Project. The ESCO shall be responsible for the security and protection of such materials and equipment delivered to the Project and not incorporated in the work. The Governing Board has found that the Project is substantially complex and therefore requires a retention amount of 10%. Within thirty (30) calendar days after the approval of each estimate for progress payment, the School will pay to the ESCO an amount equal to ninety (90) percent of the approved estimate. Payments may at any time be withheld if in the judgment of the School the work is not proceeding in accordance with the Contract Documents, the ESCO is not complying with the requirements of the Contract, stop notices have been timely filed, the estimate contains an error, or the School has incurred costs or requests reasonable financial assurances regarding defective work by the ESCO.

d. Final Payment:

Within thirty (30) days after all required work is fully completed in accordance with the Contract Documents, the ESCO shall submit a final invoice for the total value of the work completed in accordance with the Contract, which shall be subject to review and approval by the School. As required by law, School shall pay ESCO the unpaid balance of the Contract price of the work, or the whole Contract price of the work if no progress payment has been made, determined in accordance with the terms of the Contract, less such sums as may be lawfully retained under any provision of the Contract, including, but not limited to, amounts retained as liquidated damages, for stop notices, for third-party claims for which the ESCO is required to indemnify the School, for defective work and costs incurred by the School in connection therewith, or for other such claims and damages attributable to the ESCO ("Final Payment"). Prior progress estimates and payments are subject to correction in the Final Payment. Tender of the Final Payment shall constitute denial by the School of any unresolved claim. ESCO's acceptance of the Final Payment shall operate as a full and final

release to the School and its agents from any and all unasserted claims ESCO has, or may have, related to this Contract.

e. **Payments Do Not Imply Acceptance of Work:**

The granting of any progress payment or payments by the School or the receipt thereof by the ESCO shall not constitute acceptance of the work or of any portion thereof and shall in no way lessen the liability of the ESCO to replace unsatisfactory work or material, whether or not the unsatisfactory character of such work or material was apparent or detected at the time such payment was made.

f. **Retention of Sums Charged Against ESCO:**

It is mutually understood and agreed that when under any provision of this Contract the School shall charge any sums of money against the ESCO, the amount of such charge shall be deducted and retained by the School from the amount of the next succeeding progress estimate, or from any other monies due or that may become due the ESCO on account of the Contract. If on completion or termination of the Contract such monies due the ESCO are found insufficient to cover the School's charges against the ESCO, the School shall have the right to recover the balance from the ESCO or the ESCO's Sureties.

g. **Release:**

The ESCO and each assignee under an assignment in effect at the time of Final Payment shall, if required by the School, execute and deliver at the time of Final Payment and as a condition precedent to Final Payment, a release in form and substance satisfactory to and containing such exemptions as may be found appropriate by the School, discharging the School, its officers, agents and employees of and from liabilities, obligations and claims arising under this Contract.

h. **Payment to Subcontractors and Suppliers:**

The ESCO shall pay each Subcontractor and supplier promptly on receipt of each progress payment from the School for the materials, labor and equipment delivered to the site or incorporated in the work by each Subcontractor during the period for which the progress payment is made, less any retention as provided above.

i. **Stop Notice Costs:**

The School reserves the right to charge the ESCO or Surety, or to withhold from release of retention, all costs incurred by the School, including attorney's fees, for processing and defending stop notice claims.

28. MODIFICATIONS OF CONTRACT

a. **Changes in the Work:**

1). The School, before the date of acceptance of the work, may, without notice to the Sureties, order changes in the work ("Modifications"), may order extra materials and extra work in connection with the performance of the Contract, and the ESCO shall promptly comply with such orders. All Modifications must be approved by the State Fire Marshall, if applicable, as required by law.

2). If changes ordered in design, workmanship or materials are of such a nature as to increase or decrease the cost of any part of the work, the price fixed in the Contract shall be increased or decreased by such amount as represents the reasonable and proper allowance for the increase or

decrease in the cost of the work in accordance with the provisions of this Article, and any other applicable terms of the Contract, including, but not limited to, the ESCO's schedule of values and the price for allowances, if any. Except as provided by law, the **total cost of all Modifications shall not exceed ten (10) percent of the original Contract price.**

3). In the case of a disputed work item, the School may direct the ESCO to perform the disputed work at no additional cost to the School on the grounds that the work is adequately indicated in the Contract Documents, and therefore already included in the Contract price. If the ESCO maintains that the disputed work represents a modification to the Contract, ESCO may submit a claim in accordance with Article 50, Resolution of Construction Claims. Notwithstanding any dispute regarding the requirements of the Contract Documents, ESCO shall promptly and fully comply with the School's directive. ESCO's failure to do so shall be deemed a material breach of this Contract, and in addition to all other remedies, School may, at its sole discretion, hire another ESCO and/or use its own forces to complete the disputed work at ESCO's sole expense, and may deduct the cost of such work from the Contract price.

b. Cost Breakdown

When the Modification is proposed, the ESCO shall furnish a complete breakdown of actual costs of both credits and extras, itemizing materials, labor, taxes, overhead and profit. Subcontract work shall be so indicated. All costs must be fully documented. The following limitations shall apply:

1). Limitations Where Contract Price Changes are Involved:

- (a) Overhead and Profit for the ESCO. The ESCO's overhead and profit on the cost of subcontracts shall be a sum not exceeding ten percent (10%) of such costs. The ESCO's overhead and profit on the costs of work performed by the ESCO shall be a sum not exceeding fifteen percent (15%) of such costs. Overhead and profit shall not be applied to the cost of taxes and insurance by ESCO or Subcontractors or to credits. No processing or similar fees may be charged by the ESCO in connection with the Modification.
- (b) Bond Premiums. The actual rate of bond premiums as paid on the total cost (including taxes) will be allowed, but with no markup for profit and overhead.
- (c) Taxes. State and city sales taxes should be indicated. Federal excise tax shall not be included. (School will issue an exemption on request.)

2). Change Order Certification:

All change orders and requests for proposed change orders shall be deemed to include the following certification by the ESCO:

"The undersigned ESCO approves the foregoing as to the changes in work, if any, and as to the Contract price specified for each item and as to the extension of time allowed, if any, for completion of the Project as stated herein, and agrees to furnish all labor, materials, and service and to perform all work necessary to complete any additional work specified for the consideration stated herein. Submission of claims which have no basis in fact or which ESCO knows are false are made at the sole risk of the ESCO and may be a violation of the False Claims Act, as set forth in Government Code §§12650 et seq. It is understood that the changes to the Contract Documents set forth herein shall only be effective upon approval by the Governing Board of the School."

"It is expressly understood that the value of the extra work or changes expressly includes any and all of the ESCO's costs and expenses, both direct and indirect, resulting from additional time required on the Project or resulting from delay to the Project. Any costs, expenses, damages, or time extensions not included herein are deemed waived."

c. Unit Prices, Schedule of Values, or Allowances:

Where Unit Prices, a Schedule of Values, and/or Allowances are required by the Contract Documents, that pricing shall govern in computing any additions to or deductions from the Contract price on account of any added or omitted work. Unit Prices listed in the original proposal include all costs and no addition of any description will be allowed.

d. Time and Materials:

If it is impractical, because of the nature of the work, or for any other reason, to fix an increase in price in advance, the Change Order may fix a maximum price which shall not under any circumstances be exceeded, and subject to such limitation, such alteration, modification or extra shall be paid for at the actual necessary cost as determined by the sum of the following items (1) to (5) inclusive:

- 1). Labor, including premium on compensation insurance and charge for Social Security taxes, and other taxes pertaining to labor.
- 2). Material, including sales taxes and other taxes pertaining to materials.
- 3). Plant and equipment rental, to be agreed upon in writing before the work is begun. No charge for the cost of repairs to plant or equipment will be allowed.
- 4). Overhead and profit computed at fifteen percent (15%) of the total of Items (1) to (3) inclusive.
- 5). The proportionate cost of premiums on bonds computed at one and one-half percent (1-1/2%) of the total of items (1) to (4) inclusive.

If the Time and Materials work is done by a Subcontractor, the amount shall be determined as set forth above under items (1) to (5) inclusive. The ESCO's overhead and profit on the costs of subcontracts (exclusive of taxes and insurance) shall not exceed ten percent (10%) of such costs.

The School reserves the right to furnish such materials as it may deem expedient, and no allowance will be made for profit thereon. The above-described methods of determining the payment for work and materials shall not apply to the performance of any work or the furnishing of any material which, in the judgment of the School, may properly be classified under items for which prices are established in the Contract.

e. Oral Modifications:

No oral statements of any person shall in any manner or degree modify or otherwise affect the terms of the Contract.

29. INDEMNITY

ESCO shall defend with counsel acceptable to the School, indemnify and hold harmless to the full extent permitted by law, the School and its Board of Trustees, officers, agents, Project Manager, construction manager, employees and volunteers from and against any and all liability, loss, damage, claims, expenses, fines, judgments and costs (including, without limitation, attorney's fees and costs and fees of litigation) (collectively, "Liability") of every nature arising out of or in connection with ESCO's performance of the Project or its failure to comply with any of its obligations contained in these Contract Documents, except such Liability caused by the active negligence, sole negligence or willful misconduct of the School. Such indemnification shall extend to all claims, demands, or liabilities occurring after completion of the project as well as during the progress of the work. Pursuant to Public Contract Code §9201, School shall timely notify ESCO of receipt of any third-party claim relating to this Project.

30. WARRANTY OF TITLE

ESCO warrants that title to all work, materials or equipment included in a request for payment shall pass and transfer to the School whether or not they are installed or incorporated in the Project, free from any claims, liens, or encumbrances, when such payment is made to the ESCO. ESCO further warrants that no such work, materials or equipment have been purchased for work under the Contract subject to an agreement by which an interest therein or an encumbrance thereon is retained by the seller or supplier.

31. USE OF COMPLETED PARTS OF THE WORK BEFORE ACCEPTANCE

Whenever the work or any part thereof is in a condition suitable for use, and the best interest of the School requires such use, as determined by the School, the School may take possession of, connect to, open for public use, or use the work or a part thereof. When so used, maintenance and repairs due to ordinary wear and tear or vandalism will be made at School's expense. The use by the School of the work or part thereof as contemplated in this section shall in no case be construed as constituting acceptance of the work or any part thereof, including, but not limited to, the right to assess liquidated damages. Such use shall neither relieve the ESCO of any of ESCO's responsibilities under the Contract nor act as a waiver by the School of any of the conditions thereof. ESCO shall continue to maintain all insurance, including Builder's Risk insurance, on the entire Project, and diligently pursue full completion of the work.

32. GUARANTEE & WARRANTY

By signing this Contract, ESCO agrees to the following guarantee and warranty:

We hereby guarantee and warrant our work on the ECAA-Ed Energy Project for a period of ten (10) years from the date of filing of the Notice of Completion.

Panels will have a 25-year warranty.

Inverters shall have the maximum extended warranty.

ESCO shall promptly repair or replace to the satisfaction of the School any or all work that appears defective in workmanship, equipment and/or materials for whatever reason, ordinary wear and tear and unusual abuse or neglect excepted, together with any other work which may be damaged or displaced in so doing. ESCO agrees to promptly correct and remedy any failure by the ESCO to conform its work, activities, and services to the requirements of the Contract Documents.

ESCO shall provide post-construction a 10% warranty bond substantially in form of **Appendix F**, attached hereto for any work that may need repair or replacement post-installation for a period of two years from the date of filing the Notice of Completion or ESCO can provide a two-year maintenance period from the Payment and Performance bonds from the date of filing the Notice of Completion. Warranty bond shall be issued before substantial completion of project.

In the event of the ESCO's failure to comply with the above-mentioned obligations within the ten (10) calendar days of notice, or sooner if required by an emergency, ESCO hereby authorizes the School to have the defects or deficiencies repaired, remedied, corrected, and made good at ESCO's expense, and ESCO shall pay the costs and charges therefore upon demand. The warranty bond will cover these costs and charges as well for a period of two years from the date of filing the Notice of Completion.

33. PROTECTION OF WORK AND PROPERTY

a. The ESCO shall be responsible for each operation and all work on the Project, both permanent and temporary. The ESCO shall protect the work and materials from damage due to negligence, the action of the elements, the carelessness of third parties, vandalism, or any other cause whatsoever, until the final completion and acceptance of the Project. Should improper work by the ESCO be covered by another ESCO and damage or defects result, the whole work affected shall be made good by the ESCO to the satisfaction of the Project Manager and School without expense to the School. The ESCO shall take reasonable care to avoid damage to existing facilities or utilities, whether on the Project or adjacent to it, and ESCO shall be liable for any damage thereto or interruption of service due to ESCO's operations. If the ESCO encounters any facilities or utilities not shown on the drawings or not reasonably inferable there from, ESCO shall promptly notify the Project Manager about them, and shall do no further work which may cause damage to same. If it is determined that some action needs to be taken regarding facilities not shown, the ESCO will be given directives on what action to take, and any additional cost to the ESCO incurred thereby will be handled by Change Order.

b. The property limits of the area of the Project are indicated on the drawings. Except for work specifically shown or noted, ESCO shall confine ESCO's operations within the indicated property limits. The ESCO shall provide, install, and maintain all shoring, bracing and underpinning necessary to support adjacent property, streets, buildings and structures, that may be affected by building operations for this work; shall serve or cause to be served all legal notices to adjoining property owners that may be necessary for their protection; and shall protect from damage all adjacent buildings, fences, landscaping, and repair or replace any such property damaged in the course of work under the Contract.

34. USE OF ROADWAYS AND WALKWAYS

The ESCO shall not unnecessarily interfere with use of any roadway, walkway, or other facility for vehicular or pedestrian traffic, by any party entitled to use it. Wherever such interference becomes necessary for the proper and convenient performance of the work and no satisfactory detour route exists, the ESCO shall, before beginning the interference, provide a satisfactory detour, temporary bridge, or other proper facility for traffic to pass around or over the interference and shall maintain it in satisfactory condition as long as the interference continues, all without extra payment unless otherwise expressly stipulated in the Contract Documents.

35. MATERIALS

- a. Unless explicitly stated otherwise, all specified equipment and material comprising the work of this Contract, as being provided or furnished or installed, shall imply the inclusion of all components, hardware, and accessories, required for complete installation and satisfactory operation as intended by the manufacturer. Wherever the method of installation of any material is not explicitly specified, the installation shall be as recommended by manufacturer.
- b. Wherever in the Contract Documents it is provided that the ESCO shall furnish materials or equipment for which no detailed specifications are set forth, such materials or equipment shall be new and of the best grade for the purpose for which they will be used when incorporated in the work. Materials specified by reference to a number or symbol of a specific standard, such as A.S.M., Federal Specification, State Standard, Trade Association, or similar standards, shall comply with requirements in the latest revision thereof and any amendment or supplement in effect on the date of the Request for Proposals.
- c. None of the materials to be provided furnished or installed on this project shall contain asbestos or any other "hazardous substance" as that term is defined by federal or state law.

36. SUBSTITUTIONS

- a. Wherever in the drawings or Specifications a material or product is called for by trade or brand names or manufacturer and model number, alternative items of equal quality and purpose may be proposed for use by the ESCO. The burden of proof of equality is on the ESCO, and ESCO shall furnish all information and supplies necessary for the Project Manager to make a thorough evaluation of the proposed substitution. The Project Manager's decision about the equality of the proposed substitution is final, and if the proposed substitution is not approved, the ESCO shall install the item called for. Proposed substitutions and any changes in adjacent work caused by them shall be made by the ESCO at no additional cost to the School.
- b. Proposed substitutions shall be submitted sufficiently before actual need to allow time for thorough evaluation. Substitutions shall not be proposed because submittals were not made early enough to avoid delay. Project Manager's review of substitutions shall not relieve the ESCO from complying with the requirements of the drawings and Specifications. Requests for substitution will be considered if received within 30 days after receipt of the Notice of Award. Requests received more than 30 days after receipt of the Notice of Award may be considered or rejected at the discretion of the Project Manager. ESCO shall identify the product, or the fabrication or installation method to be replaced in the request. ESCO shall also provide complete documentation showing compliance with the requirements for substitutions, as set forth herein, and the following information, as appropriate:
 - Product Data, including Drawings and descriptions of products, fabrication, and installation procedures.
 - Samples, where applicable or requested.
 - A detailed comparison on the same page of significant qualities of the proposed substitution with those of the Work specified. Significant qualities may include elements such as size, weight, durability, performance and visual effect. All differences in products shall be noted.

- A statement indicating the substitution's effect on the ESCO's Construction Schedule compared to the schedule without approval of the substitution. Indicate the effect of the proposed substitution on overall Contract Time.
- Certification by the ESCO that the substitution proposed complies in every significant respect to that required by the Contract Documents, and that it shall:
 - Be equal to or better in every significant respect to specified material or product and shall perform adequately in the intended application.
 - Provide the same or greater warranty for the substitution as for the specified product.
 - Provide the same required fire rating for the substitution as for the specified product.
 - Coordinate installation and make changes to other Work, which may be required for the Work to be complete with no additional costs to Owner.

c. In the event ESCO makes substitutions in materials, equipment, or designs, with or without the School's approval, other than those authorized herein, the ESCO shall then assume full responsibility for the effects of such substitutions on the entire project, including the design, and shall reimburse the School for any charges resulting from such substitutions, including any charges for modifications in the work of other trades, and including any charges for additional design and review, plus reasonable and customary mark-ups.

37. TESTING

a. Materials, equipment, or other work requiring tests may be specified in the Contract Documents, and they shall be adequately identified and delivered to the site in ample time before intended use to allow for testing. If such materials, equipment, or other work should be covered without required testing and approval, they shall be uncovered at the ESCO's expense, including any repairs or replacement resulting there from. The ESCO shall notify the School and Project Manager when and where such materials, equipment or other work are ready for testing, and ESCO shall bear the cost of making them available for testing. The ESCO shall notify the School and Project Manager sufficiently before the need for testing so as to cause no delay in the work and, in any case, at least forty-eight (48) hours prior to the need for testing.

b. The cost of initial tests called for will be paid by the School and will be performed by independent testing consultants retained by the School. All other tests and inspections specified or otherwise required to substantiate compliance with specified requirements for quality of material or performance of operation shall be paid for by the ESCO. If retesting or additional testing is necessary because of substandard initial test results, the costs thereof shall be paid by the ESCO, including any repairs or replacement resulting there from.

38. INSPECTION

a. All materials, equipment and workmanship used in the work of the Project shall be subject to inspection or testing at all times and locations during construction and/or manufacture. The School's and Project Manager's authorized representatives and representatives of other agencies having authority over the work shall have access to the work for the above purposes at all reasonable times and locations. Any material or work found to be unsatisfactory or not according to the Contract

Documents shall be replaced with the correct material or work and the defective items promptly removed, all at the ESCO's expense, when directed to do so by any of the above-named persons having authority over the work. The cost of review time and analysis by the Project Manager or other School consultants necessitated by incomplete or defective work by the ESCO shall be charged to the ESCO.

b. Inspection and testing by the School or its representatives shall not relieve the ESCO from complying with the requirements of the Contract Documents. The ESCO is responsible for its own quality control.

c. Whenever required by the School or Project Manager, the ESCO shall furnish all tools, labor and materials necessary to make an examination of work in place by uncovering the same. Should such work be found unsatisfactory, the cost of examination and reconstruction shall be paid by the ESCO. Should such work be found satisfactory, the cost of examination and reconstruction of the work shall be paid by Change Order unless the ESCO improperly covered the work before it could be inspected or tested. If the ESCO considers it necessary or desirable to work on Saturday, Sunday or a holiday, ESCO shall seek written approval from the School at least forty-eight (48) hours before the commencement of such work.

39. CLEANUP

a. The ESCO shall maintain the premises and area of the work shall be in a reasonably clean condition. No burning of rubbish on-site shall be allowed. The ESCO shall control dust on the site by sprinkling at whatever intervals are necessary to keep it laid down and shall take measures to prevent dust and debris from being accidentally transported outside the area of the work.

b. Final cleaning, such as sweeping, dusting, vacuuming, dry and wet mopping, polishing, sealing, waxing and other finish operations normally required on newly installed work shall be taken to indicate the finished conditions of the various new and existing surfaces to restore area to condition at the time of acceptance. Prior to the time of acceptance, all marks, stains, fingerprints, dust, dirt, splattered paint, and blemishes resulting from the various operations shall be removed throughout the Project. Stair treads and risers shall be wet mopped. Glass shall be left clean and polished both inside and outside. Plumbing fixtures and light fixtures shall be washed clean. Hardware and other unpainted metals shall be cleaned, and all building papers and other temporary protections shall be removed throughout the building, or portion of the building where ESCO was involved, all to the satisfaction of the Project Manager and School. The exterior of the buildings, playfields, exterior improvements, planting spaces, and other work areas shall be similarly clean and in good order.

40. CONSTRUCTION WASTE MANAGEMENT

The ESCO shall submit the Waste Management Plan to the Project Manager within 15 calendar days after receipt of the Notice to Proceed, or prior to any waste removal, whichever occurs first. The ESCO shall promptly revise and resubmit the Plan as required by the Project Manager. Review of the ESCO's Waste Management Plan will not relieve the ESCO of responsibility for compliance with applicable environmental regulations or meeting Project diversion requirements.

a. Scope

1). This Article includes requirements for the diversion by the ESCO of construction and demolition debris from landfills. The ESCO shall develop and implement a Waste Management Plan as specified herein. The ESCO shall take a pro-active, responsible role in the management of

construction and demolition waste and require all Subcontractors, vendors, and suppliers to participate in the effort.

2). The School has established that this Project shall generate the least amount of waste practicable, and those processes shall be utilized that ensure the generation of as little waste as possible due to over-packaging, error, poor planning, breakage, mishandling, contamination or other factors.

3). As much of the waste materials as economically feasible shall be reused, salvaged, or recycled. Waste disposal in landfills shall be minimized.

4). The ESCO is encouraged to use waste hauling companies that separate recyclable materials. The ESCO shall work with its waste haulers in providing other recycling methods as appropriate.

5). The ESCO is responsible for implementation of any special programs involving rebates or similar incentives related to the recycling of waste. Revenues or other savings obtained for salvage or recycling accrue to the ESCO.

b. References

1). "Builders' Guide to Reuse and Recycling, A Directory for Construction and Demolition Materials."

2). "Construction Site Recycling, a Guide for Building ESCOs ". For a copy of the guide call 1-888-442-2666 or go to www.recycleworks.org.

3). "Where to Recycle Construction and Demolition Debris." For a copy of the guide call 1-888-442-2666 or go to www.recycleworks.org.

c. Definitions

1). General: Construction and demolition waste includes products of demolition or removal, excess or unusable construction materials, packaging materials for construction products, and other materials generated during the construction process but not incorporated into the work.

2). Divert" means to use material for any lawful purpose other than disposal in a landfill or transfer facility for disposal

3). "Recycling Service" means an off-site service that provides processing of material and diversion from a landfill.

4). "Hauler" means the entity that transports construction and demolition debris to either a landfill or a recycling service.

d. Compliance with Regulatory Requirements

1). The ESCO shall perform all handling, storage, transportation, and disposal of construction debris in compliance with all applicable Federal, State, regional, and local statutes, laws, regulations, rules, ordinance, codes, and standards.

2). Nothing stated on the drawings, in this Article 40 or in any other provision of the Contract Documents shall be construed as allowing work that is not in strict compliance with all applicable Federal, State, regional, and local statutes, laws, regulations, rules, ordinances, codes and standards.

e. Performance Requirement

The ESCO shall divert a minimum of 50 percent (50%) of the total Project construction and demolition waste from landfills.

f. Quality Control

1). General:

i) The ESCO shall not permit materials designated for diversion to become contaminated or to contaminate the site or surrounding areas.

2). Training and Coordination:

- i) The ESCO shall designate an on-site party [or parties] who will be responsible for instructing workers and Subcontractors and overseeing and documenting the results of the Waste Management Plan for the Project.
 - ii) The ESCO shall furnish copies of the Waste Management Plan to all on-site supervisors, each Subcontractor, and the School's representative.
 - iii) The ESCO shall include construction waste management as an item on the agenda of all progress meetings.
- 3). The Waste Management Plan:
 - i) The ESCO shall prepare a Waste Management Plan for diverting the specified percentage of construction debris from landfills, including written and graphic information indicating how the waste will be diverted.
 - ii) Include in the plan both on-site recycling of construction debris and off-site diversion from landfills.
 - iii) Identify the means and methods for collecting and separating each type of debris deemed reusable or recyclable.
 - iv) List the off-site recycling service and hauler of each designated debris item who has agreed to accept and divert that item from the landfill in the proposed quantities anticipated. List the service and hauler company name, address, telephone number, and persons contacted.
 - v) List the name of individuals on the ESCO's staff responsible for waste prevention and management.
 - vi) List the actions that will be taken to reduce solid waste generation, including coordination with Subcontractors to ensure awareness and participation.
 - vii) Describe the specific approaches to be used in recycling/reuse of the various materials generated, including the areas on site and equipment to be used for processing, sorting, and temporary storage of wastes.
 - viii) Characterize the waste to be generated, including estimated types and quantities. Name the landfills and/or incinerator to be used.
 - ix) List the specific waste materials that will be salvaged for resale, salvaged, and reused on the Project, salvaged and stored for reuse on a future project, or recycled. Recycling facilities that will be used shall be identified by name, location, and phone number.
 - x) Identify the materials that cannot be recycled or reused with an explanation or justification, to be approved by the Project Manager.
- g. Plan Implementation
 - 1). The ESCO shall implement the approved Waste Management Plan.
 - 2). The ESCO shall maintain a log of each load and of each category of waste that is diverted from the landfill. The ESCO shall separately log the debris sent to a Class III landfill and materials sent to recycling facilities.
 - 3). The ESCO shall include in the log the type of load, load weight, name of the hauling service, recycling service or landfill, and the date accepted by the recycling service or by the landfill.
 - 4). The ESCO shall retain and make available all weight tickets and copies of receipts and invoices relating to the implementation of the Plan.
 - 5). The School reserves the right to audit the log at any time.
- h. Material Handling
 - 1). Designate a specific area or areas on site to facilitate the separation of materials for potential reuse, salvage, recycling, and return. Clearly mark bins for each category of waste.
 - 2). Keep waste bins and pile areas neat and clean. Do not contaminate non-recyclable waste with materials designated for reuse or recycling.

i. ESCO's Responsibilities

- 1). Provide on-site instruction of the appropriate separation, handling, recycling, salvage, reuse, and return methods to be used by all parties at the appropriate stages of the Project.
- 2). Separate, store, protect, and handle at the site identified recyclable and salvageable waste products in a manner that maximizes recyclability and salvageability of identified materials.
- 3). Provide the necessary containers, bins, and storage areas to facilitate effective waste management.
- 4). Provide barriers and enclosures around recyclable material storage areas which are nonhazardous and recyclable or reusable and which shall be located away from construction traffic.
- 5). Provide adequate space for pick-up and delivery.
- 6). Use cleaning materials that are nonhazardous and biodegradable.

41. INSTRUCTIONS AND MANUALS

ESCO will provide one electronic copy of all maintenance instructions application/installation instructions and service manuals called for in the Specifications shall be provided by the ESCO to the project manager for the project record. These shall be complete as to drawings, details, parts lists, performance data and other information that may be required for the School to easily maintain and service the materials and equipment installed under this Contract. All manufacturers' application/installation instructions shall be given to the Project Manager at least ten (10) days prior to first material application or installation of the item. The maintenance instructions and manuals, along with any specified guarantees, shall be delivered to the Project Manager for review prior to submitting to School, and the ESCO or appropriate Subcontractors shall instruct School's personnel in the operation and maintenance of the equipment prior to final acceptance of the Project. All documentation must be received by Project Manager within thirty (30) calendar days after School's Notice of Completion.

42. AS-BUILT DRAWINGS

The ESCO and all Subcontractors shall maintain on the work site a separate complete set of contract drawings which will be used solely for the purpose of recording changes made in any portion of the work during the course of construction, regardless of the reason for the change. As changes occur, there will be included or marked on this record set on a daily basis, if necessary, to keep them up to date at all times. Actual locations to scale shall be identified on the drawings for all runs of mechanical and electrical work, including all site utilities, installed underground, in walls, floors, and furred spaces, or otherwise concealed. Deviations from the drawings shall be shown in detail. All main runs, whether piping, conduit, duct work, drain lines, etc., shall be located in addition by dimension and elevation. Progress payments may be delayed or withheld until such time as the record set is brought up to date to the satisfaction of the Project Manager. The ESCO shall verify that all changes in the work are included in the AS-BUILT" drawings and deliver the complete set thereof to the Project Manager for review and approval within thirty (30) calendar days after School's Notice of Completion. School's acceptance and approval of the "AS-BUILT" drawings are a necessary condition precedent to the release of the final retention.

43. SUBSTITUTION OF SECURITIES

a. Pursuant to Public Contract Code section 22300, ESCO may request in writing that it be allowed at its own expense to substitute securities for moneys withheld by School to ensure performance under this Contract. Only securities listed in Government Code Section 16430 and bank or savings and loan certificates of deposit, interest-bearing demand deposit accounts standby letters

of credit, or any other security mutually agreed to by ESCO and School shall qualify under this Article. Securities equivalent to the amount withheld shall be deposited with the School or with a state or federally chartered bank in California as the escrow agent. Upon satisfactory completion of the Contract and on written authorization by the School, the securities shall be returned to ESCO. ESCO shall be the beneficial owner of the securities and shall receive any interest thereon. The ESCO may alternatively request School to make payment of retentions earned directly to the escrow agent at the expense of the ESCO.

b. At the expense of the ESCO, the ESCO may direct the investment of the payments into securities and the ESCO shall receive the interest earned on the investments upon the same terms provided for above for securities deposited by ESCO. Upon satisfactory completion of the contract, ESCO shall receive from the escrow agent all securities, interest, and payments received by the escrow agent from the School. The ESCO shall pay to each Subcontractor, not later than 20 days of receipt of payment, the respective amount of interest earned, net of costs attributed to retention withheld from each Subcontractor, on the amount of retention.

c. Any escrow agreement entered into pursuant to this Article shall comply with Public Contract Code section 22300 and shall be subject to approval by School's counsel.

44. NO DISCRIMINATION

It is the policy of the School that, in connection with all work performed under this public works contract, there shall be no discrimination against any prospective or active employee, or any other person engaged in the work because of actual or perceived race, color, ancestry, national origin, ethnic group identification, religion, sex, gender, sexual orientation, age, physical or mental disability, or marital status. The ESCO agrees to comply with applicable Federal and California laws including, but not limited to, the California Fair Employment Practice Act, beginning with Government Code §12900, Government Code §11135, and Labor Code §§ 1735, 1777.5, 1777.6 and 3077.5. In addition, the ESCO agrees to require like compliance by all Subcontractors and suppliers.

45. LABOR STANDARDS

a. Work Hours:

In accordance with Labor Code section 1810, eight (8) hours of labor shall constitute a legal day's work under this Contract. ESCO and any Subcontractor shall pay workers overtime pay as required by Labor Code section 1815. The ESCO shall pay each worker, laborer, mechanic, or persons performing work under this Contract at a rate not less than the prevailing wage for each craft or classification covering the work actually performed.

b. Penalty:

ESCO shall forfeit to School as a penalty the sum of twenty-five dollars (\$25.00) for each worker employed in the execution of this Contract by ESCO or any Subcontractor for each calendar day during which the worker is required or permitted to work more than eight (8) hours in any one (1) calendar day or more than forty (40) hours per calendar week in violation of Article 3, Division 2, Part 7, Chapter 1 of the California Labor Code.

c. Employment of Apprentices:

ESCO shall comply with Labor Code §§1773.3, 1777.5 and 1777.6, and 3077 et. seq., each of which is incorporated by reference into this Contract. These sections require that ESCOs and Subcontractors employ apprentices in apprenticeable occupations in a ratio of not less than one (1) hour of apprentice work for every five (5) hours of labor performed by a journeyman, unless an exception is granted and that ESCOs and Subcontractors shall not discriminate against otherwise qualified employees as apprentices on any public works solely on the ground of actual or perceived race, religion, color, national origin, ethnic group identification, sex, gender, sexual orientation, age, or physical or mental disability. Only apprentices who are in training under written apprenticeship occupations shall be employed. The responsibility for compliance with these provisions for all apprenticeable occupations rests with ESCO.

d. The ESCO shall be knowledgeable of and comply with Labor Code sections 1727, 1773.5, 1775, 1777, 1777.5, 1810, 1813, 1860, including all amendments thereto; each of these sections is incorporated by reference into this Contract.

46. GENERAL RATE OF PER DIEM WAGES

a. On File:

As required by Labor Code section 1773.2, the School has available copies of the general prevailing rate of per diem wages for workers employed on public work as determined by the Director of the Department of Industrial Relations, which shall be available to any interested party on request. ESCO shall post a copy of the document at each job site.

b. Prevailing Wage Rate:

The ESCO and each Subcontractor shall pay each worker performing work under this Contract at a rate not less than the prevailing wage as defined in Labor Code section 1771 and 1774 and Section 16000(a) of Title 8, California Code of Regulations.

c. Penalty:

In accordance with Section 1775 of the Labor Code, the ESCO shall forfeit to the School as penalty, the sum of fifty dollars (\$50.00) for each calendar day, or portion thereof, for each worker paid less than the prevailing wage rates, as determined by the Director of the California Department of Industrial Relations, for any work done under this Contract by ESCO or by any Subcontractor. ESCO shall also pay each worker the difference between the stipulated prevailing wages rates and the amount actually paid to such worker.

47. RECORD KEEPING

a. The ESCO agrees to comply with the provisions of Sections 1776 and 1812 of the Labor Code. The ESCO and each Subcontractor shall keep or cause to be kept an accurate record showing the names, addresses, social security numbers, work classifications, straight time and overtime hours worked each day and week of all workers employed by ESCO in connection with the execution of this Contract or any subcontract there under and showing the actual per diem wages paid to each of such workers. These records shall be certified and shall be open at all reasonable hours to the inspection of the School awarding the Contract, its officers and agents, and to the Chief of the Division of Labor Statistics and Law Enforcement of the State Department of Industrial Law Enforcement of the State Department of Industrial Relations, and his or her other deputies and agents.

b. In addition, copies of the above records shall be available as follows:

- 1). A certified copy of an employee's payroll record shall be made available for inspection or furnished to the employee or his or her authorized representative on request;
- 2). A certified copy of all payroll records shall be made available for inspection or furnished upon request to the School, the Division of Labor Standards Enforcement, and the Division of Apprenticeship Standards of the Department of Industrial Relations;
- 3). A certified copy of all payroll records shall be made available upon request by the public for inspection or copies thereof made; provided, however, that a request by the public shall be made through either the School, the Division of Apprenticeship Standards, or the Division of Labor Standards Enforcement. If the requested payroll records have not been previously provided, the requesting party shall, prior to being provided the records, reimburse the costs of the ESCO, Subcontractors, and the entity through which the request was made. The public shall not be given access to the records at the principal office of the ESCO.

c. The ESCO shall file a certified copy of the records with the entity requesting the records within ten days after receipt of a written request. Any copy of records made available for inspection as copies and furnished upon request to the public or any public agency by the School, shall be marked or obliterated in such a manner as to prevent disclosure of an individual's name, address, and social security number. The name and address of the ESCO awarded the Contract or performing the Contract shall not be marked or obliterated.

d. The ESCO shall inform the Owner of the location of the records, including the street address, city, and county, and shall, within five working days, provide a notice of a change of location and address.

e. In the event of noncompliance with the requirements of this section, the ESCO shall have ten days in which to comply subsequent to receipt of written notice specifying in what respects the ESCO must comply with this section. Should noncompliance still be evident after the ten-day period, the ESCO shall, as a penalty to the School, forfeit one hundred dollars (\$100.00) for each calendar day, or portion thereof, for each worker, until strict compliance is effectuated. Upon the request of the Division of Apprenticeship Standards or the Division of Labor Standards Enforcement, these penalties shall be withheld from progress payments then due.

f. Responsibility for compliance with this provision shall be with the ESCO.

48. PROJECT COMPLETION

a. When all of the work to be performed under this Contract is has been fully completed, the ESCO shall notify the Project Manager and School, in writing, setting a date for inspection. The ESCO and Subcontractor representatives shall attend the inspection. As a result of this inspection, the Project Manager will prepare a list of items ("punch list") that are incomplete or not installed according to the Contract Documents. Failure to include items on this list does not relieve the ESCO from fulfilling all requirements of the Contract Documents.

b. The Project Manager will promptly deliver the punch list to the ESCO, and it will include a period of time by which the ESCO shall complete all items listed thereon. On completion of all items on the punch list, verified by a final inspection, and all other Contract requirements, so that Final Completion has been achieved to the School's satisfaction, the School will file a Notice of

Completion with the County Recorder. Payment of retention from the Contract, less any sums withheld pursuant to the terms of this Contract or applicable law, shall not be made sooner than thirty-five (35) calendar days after the date of filing of Notice of Completion.

c. School reserves the right to occupy buildings and/or portions of the site at any time before Completion, and occupancy shall not constitute final acceptance of any part of the Work covered by the Contract Documents, nor shall such occupancy extend the date specified for completion of the Work. Beneficial occupancy of building(s) does not commence any warranty period or entitle ESCO to any additional compensation due to such occupancy or affect in any way or amount ESCO's obligation to pay liquidated damages for failure to complete the Project on time.

49. TRENCHING OR OTHER EXCAVATIONS

a. Excavations or Trenches Deeper than Four Feet:

If the project involves digging trenches or other excavations that extend deeper than four feet, the following provisions shall be a part of this Contract:

1). The ESCO shall promptly, and before the following conditions are disturbed, provide written notice to the School if the ESCO finds any of the following conditions:

(a) Material that the ESCO believes may be a hazardous waste, as defined in Section 25117 of the Health and Safety Code, which is required to be removed to a Class I, Class II, or Class III disposal site in accordance with the provisions of existing law.

(b) Subsurface or latent physical conditions at the site which are different from those indicated or expected.

(c) Unknown physical conditions at the site of any unusual nature or which are materially different from those ordinarily encountered and generally recognized as inherent in work which the ESCO generally performs.

2). In the event that the ESCO notifies the School that ESCO has found any of the conditions specified in subparagraphs (a), (b) or (c), above, the School shall promptly investigate the condition(s). If the School finds that the conditions are materially different or that a hazardous waste is present at the site which will affect the ESCO's cost of, or the time required for, performance of the Contract, the School shall issue a change order in accordance with the procedures set forth in this Contract.

3). In the event that a dispute arises between the School and the ESCO regarding any of the matters specified in Paragraph (2), above, the ESCO shall proceed with all work to be performed under the Contract and the ESCO shall not be excused from completing the Project as provided in the Contract. In performing the work pursuant to this Paragraph, the ESCO retains all rights provided by Article 50 which pertains to the resolution of disputes between the contracting parties.

b. Regional Notification Center:

The ESCO, except in an emergency, shall contact the appropriate regional notification center at least two (2) days prior to commencing any excavation if the excavation will be conducted in an area that is known, or reasonably should be known, to contain subsurface installations other than the underground facilities owned or operated by the School, and obtain an inquiry identification number from that notification center. No excavation shall be commenced and/or carried out by the ESCO unless an inquiry identification number has been assigned to the ESCO or any Subcontractor and the

ESCO has given the School the identification number. Any damages or delays arising from ESCO's failure to make appropriate notification shall be at the sole risk and expense of the ESCO and shall not be considered for an extension of the Contract time.

c. Existing Utility Lines:

- 1). Pursuant to Government Code section 4215, the School assumes the responsibility for removal, relocation, and protection of main or trunk utility lines and facilities located on the construction site at the time of commencement of construction under this contract with respect to any such utility facilities that are not identified in the plans and Specifications. ESCO shall not be assessed for liquidated damages for delay in completion of the Project caused by the failure of the School or the owner of a utility to provide for removal or relocation of such utility facilities.
- 2). Locations of existing utilities provided by the School shall not be considered exact, but approximate within reasonable margin and shall not relieve ESCO of responsibilities to exercise reasonable care nor costs of repair due to ESCO's failure to do so. The School shall compensate ESCO for the costs of locating and repairing damage not due to the failure of ESCO to exercise reasonable care and removing or relocating such utility facilities not indicated in the plans and Specifications with reasonable accuracy.
- 3). No provision herein shall be construed to preclude assessment against ESCO for any other delays in completion of the project. Nothing in this Section shall be deemed to require the School to indicate the presence of existing service laterals, appurtenances, or other utility lines, with the exception of main or trunk lines, whenever the presence of such utilities on the site of the construction Project can be inferred from the presence of other visible facilities, such as buildings, meter, and junction boxes, on or adjacent to the site of the construction.
- 4). If ESCO, while performing work under this Contract, discovers utility facilities not identified by the School in the project plans and Specifications, ESCO shall immediately notify the School and the utility in writing. The cost of repair for damage to above-mentioned visible facilities without prior written notification to the School shall be borne by the ESCO.

d. Prompt Notification:

ESCO understands, acknowledges, and agrees that the purpose for prompt notification to the School pursuant to these provisions is to allow the School to investigate the condition(s) so that the School shall have the opportunity to decide how the School desires to proceed as a result of the conditions. Accordingly, failure of ESCO to promptly notify the School in writing, pursuant to these provisions, shall constitute ESCO's waiver of any claim for damages incurred as a result of the conditions.

e. Trenches Five Feet and Deeper:

Pursuant to Labor Code section 6705, if the contract price exceeds \$25,000 and involves the excavation of any trench or trenches five (5) feet or more in depth, the ESCO shall, in advance of excavation, promptly submit to the School and/or a registered civil or structural engineer employed by the School or Project Manager, a detailed plan showing the design of shoring for protection from the hazard of caving ground during the excavation of such trench or trenches.

50. RESOLUTION OF CONSTRUCTION CLAIMS

a. Public work claims of \$375,000 or less between the ESCO and the School are subject to the provisions of Article 1.5 (commencing with §20104) of Chapter 1 of Part 2 of the Public Contract Code ("Article 1.5 claim"). For purposes of Article 1.5, "public work" has the same meaning as set

forth in §§3100 and 3106 of the Civil Code; "claims" means a separate demand by ESCO for a time extension or payment of money or damages arising from work done by or on behalf of ESCO pursuant to the Contract and payment of which is not otherwise expressly provided for or the claimant is not otherwise entitled to or the amount of the payment which is disputed by the School.

b. All claims shall be submitted on or before the date of the Final Payment and shall include all documents necessary to substantiate the claim. School shall respond in writing within 45 days of receipt of claim if the claim is less than or equal to \$50,000 ("\$50,000 claim") or within 60 days if the claim is over \$50,000 but less than or equal to \$375,000 ("50,000 - \$375,000 claim"). In either case, School may request in writing within 30 days of receipt of claim any additional documentation supporting the claim or relating to any defenses to the claim which the School may have against the ESCO. Any additional information shall be requested and provided upon mutual agreement of the School and the ESCO. School's written response to the claim shall be submitted to ESCO within 15 days after receipt of the further documentation for \$50,000 claims or within 30 days after receipt of the further documentation for \$50,000 - \$375,000 claims or within a period of time no greater than that taken by the ESCO in producing the additional information, whichever is greater.

c. Within 15 days of receipt of the School's response, if ESCO disputes the School's written response, or within 15 days of the School's failure to respond within the time prescribed, the ESCO shall provide written notification to School demanding an informal conference to meet and confer ("conference") to be scheduled by School within 30 days. Following the conference, if any claim or portion remains in dispute, the ESCO may file a claim as provided in Chapter 1 (commencing with §900) and Chapter 2 (commencing with §910) of Part 3 of Division 3.6 of Title 1 of the Government Code. For purposes of those provisions, the period of time within which a claim must be filed is tolled from the time the claimant submits a written claim pursuant to this section until the time that claim is denied as a result of the conference process, including any period of time utilized by the meet and confer process.

d. Pursuant to Public Contract Code §20104.2(f), this section does not apply to tort claims and does not change the period for filing claims or actions specified by Chapter 1 (commencing with §900) and Chapter 2 (commencing with §910) of Part 3 of Division 3.6 of Title 1 of the Government Code.

e. If a civil action is filed, within 60 days, but no earlier than 30 days, following the filing of responsive pleadings, the court shall submit the matter to nonbinding mediation unless waived by mutual stipulation of both parties. The mediation process shall provide that both parties select a disinterested third person mediator within 15 days, shall be commenced within 30 days of the submittal, and shall be concluded within 15 days of the commencement of the mediation unless time is extended upon a good cause showing to the court or by stipulation of the parties. If the parties fail to select a mediator within the 15-day period, any party may petition the court to appoint the mediator.

f. If the matter remains in dispute, the case shall be submitted to judicial arbitration as set forth in Public Contract Code §§20104.4 (b)(1) through (b)(3).

g. For any claim in excess of \$375,000, the ESCO and the School shall follow the same process as for an Article 1.5 claim. The School will forward a response within 60 days of submittal of any such claim. Judicial arbitration is not required for claims in excess of \$375,000. Claims shall also be processed consistent with Public Contract Code section 9204, which provides processing timelines and procedures, and requires that undisputed claims be promptly paid in accordance with this code provision.

h. In addition, for all unresolved claims that the ESCO wishes to pursue, the ESCO shall file a timely claim pursuant to the Government Claims Act and shall otherwise comply with the procedures set forth in that Act prior to commencing any litigation against the School. The accrual date for any such claim is the date the dispute or controversy first arose regarding the issues raised in the claim.

i. "The date of Final Payment," as used in this Article 50, means the date the public entity is required to release retention proceeds in accordance with Public Contract Code §7107 regardless of whether any payment is made to the ESCO at that time.

j. The claims required by this Article are jurisdictional and conditions precedent to the commencement of any further legal proceedings. Strict compliance with all filing deadlines is mandatory.

51. DISABLED VETERANS PARTICIPATION GOALS (Applies to K-12 Schools only.)

In accordance with Education Code §17076.11, this School has a participation goal for disabled veteran business enterprises ("DVBE") of at least 3 percent (3%) per year of the overall dollar amount of funds allocated to the School by the State Allocation Board pursuant to the Leroy F. Greene School Facilities Act of 1998 for construction or modernization and expended each year by the School. Prior to, and as a condition precedent for final payment under any contract for such project, the ESCO shall provide appropriate documentation to the School identifying the amount paid to DVBE in conjunction with the Contract, so that the School can assess its success at meeting this goal.

52. RETENTION OF DVBE RECORDS (Applies to K-12 Schools only.)

The ESCO agrees that, for all contracts subject to DVBE participation goals, the State and the School have the right to review, obtain and copy all records pertaining to performance of the contract in accordance with DVBE requirements. The ESCO agrees to provide the State or the School with any relevant information requested and shall permit the State or School access to its premises upon reasonable notice for purposes of interviewing employees and inspecting records. The ESCO agrees to maintain such records for a period of three years after final payment under the Contract.

53. FINGERPRINTING (Applies to K-12 Schools only.)

School Determination of Fingerprinting Requirement Application

The School has considered the totality of the circumstances concerning the Project and has determined that the ESCO and ESCO's employee (which includes Subcontractor employees):

_____ are subject to the requirements of Education Code §45125.2 and Paragraph (a) below, is applicable.

 X are not subject to the requirements of Education Code §45125.2, and Paragraph (b) below, is applicable.

a. Contracts for Construction, Reconstruction, Rehabilitation or Repair of a School Facility Involving More than Limited Contact with Students (§45125.2)

By execution of the Contract, the ESCO acknowledges that ESCO is entering into a contract for the construction, reconstruction, rehabilitation, or repair of a school facility where the ESCO and/or ESCO's employees will have more than limited contact with students and the services to be provided do not constitute an emergency or exceptional situation. In accordance with Education Code §45125.2 the ESCO shall, at ESCO's own expense, (1) install a physical barrier to limit contact with students by ESCO and/or ESCO's employees, and/or (2) provide for the continuous

supervision and monitoring of the ESCO and/or ESCO's employees by an employee of the ESCO who has received fingerprint clearance from the California Department of Justice, and/or (3) provide for the surveillance of the ESCO and ESCO's employees by a School employee.

b. **Contracts for Construction, Reconstruction, Rehabilitation or Repair of a School Facility Involving Only Limited Contact with Students (§45125.2)**

By execution of the Contract, the ESCO acknowledges that ESCO is entering into a contract for the construction, reconstruction, rehabilitation, or repair of a school facility involving only limited contact with students. Accordingly, the parties agree that the following conditions apply to any work performed by the ESCO and ESCO's employees on a school site: (1) ESCO and ESCO's employees shall check in with the school office each day immediately upon arriving at the school site; (2) ESCO and ESCO's employees shall inform school office staff of their proposed activities and location at the school site; (3) Once at such location, ESCO and ESCO's employees shall not change locations without contacting the school office; (4) ESCO and ESCO's employees shall not use student restroom facilities; and (5) If ESCO and/or ESCO's employees find themselves alone with a student, ESCO and ESCO's employees shall immediately contact the school office and request that a member of the school staff be assigned to the work location.

54. LABOR COMPLIANCE PROGRAM

If this Contract is for a public works project over \$25,000 or for a maintenance project over \$15,000, ESCO acknowledges that the project is subject to compliance monitoring and enforcement by the California Department of Industrial Relations in accordance with California Labor Code sections 1725.5 and 1770 *et seq.* All contractors and subcontractors working at the site shall be duly registered with the Department of Industrial Relations at time of bid opening and at all relevant times. Proof of registration shall be provided as to all such contractors prior to the commencement of any work. ESCO shall coordinate with the School to ensure that DIR is advised of the award of the construction contract in a timely manner by filing form PWC-100 with DIR within thirty days of award of the contract, but no later than the first day in which the ESCO has workers employed upon the project.

55. DRUG-FREE WORKPLACE CERTIFICATION

ESCO certifies all of the following:

a. ESCO is aware of the provisions and requirements of California Government Code §§ 8350 *et seq.*, the Drug Free Workplace Act of 1990.

b. ESCO is authorized to certify, and does certify, that a drug free workplace will be provided by doing all of the following:

- 1). Publishing a statement notifying all employees that the unlawful manufacture, distribution, dispensation, possession, or use of a controlled substance is prohibited in ESCO's workplace and specifying actions which will be taken against employees for a violation of the prohibition;
- 2). Establishing a drug-free awareness program to inform employees about all of the following:
 - (i) The dangers of drug abuse in the workplace;
 - (ii) ESCO's policy of maintaining a drug-free workplace;
 - (iii) The availability of drug counseling, rehabilitation, and employee-assistance programs; and
 - (iv) The penalties that may be imposed upon employees for drug abuse violations;
- 3.) Requiring that each employee engaged in the performance of Work on the Project be given a copy of the statement required by subdivision (a), above, and that as a condition of

employment by ESCO in connection with the Work on the Project, the employee agrees to abide by the terms of the statement.

c. ESCO understands that if the School determines that ESCO has either: (a) made a false certification herein, or (b) violated this certification by failing to carry out and to implement the requirements of Government Code §§ 8350 et seq., the Contract is subject to termination, suspension of payments, or both. ESCO further understands that, should ESCO violate the terms of the Drug-Free Workplace Act of 1990, ESCO may be subject to debarment in accordance with the provisions of Government Code §§ 8350, et seq.

56. PROVISIONS REQUIRED BY LAW DEEMED INSERTED

Every provision of law and clause required by law to be inserted in this Contract shall be deemed to be inserted, and this Contract shall be read and enforced as though it were included, and if through mistake or otherwise any provision is not inserted or is not correctly inserted, upon application of either party the Contract shall be amended to make the insertion or correction. All references to statutes and regulations shall include all amendments, replacements, and enactments on the subject which are in effect as of the date of this Contract.

57. GENERAL PROVISIONS

a. Assignment and Successors:

Neither party may transfer or assign its rights or obligations under the Contract Documents, in part or in whole, without the other party's prior written consent. The Contract Documents are binding on the heirs, successors, and permitted assigns of the parties hereto.

b. Third Party Beneficiaries:

There are no intended third-party beneficiaries to the Contract.

c. Choice of Law and Venue

The Contract Documents shall be governed by California law, and venue shall be in the Superior Court of the county in which the project is located, and no other place.

d. Severability

If any provision of the Contract Documents is determined to be illegal, invalid, or unenforceable, in part or in whole, the remaining provisions, or portions of the Contract Documents shall remain in full force and effect.

e. Entire Agreement

The Contract Documents constitute the final, complete, and exclusive statement of the terms of the agreement between the parties regarding the subject matter of the Contract Documents and supersedes all prior written or oral understandings or agreements of the parties.

f. Waiver

No waiver of a breach, failure of any condition, or any right or remedy contained in or granted by the provisions of the Contract Documents shall be effective unless it is in writing and signed by the party waiving the breach, failure, right, or remedy. No waiver of any breach, failure, right, or remedy shall be deemed a waiver of any other breach, failure, right, or remedy, whether or not similar, nor shall any waiver constitute a continuing waiver unless the writing so specifies.

g. Headings

The headings in the Contract Documents are included for convenience only and shall neither affect the construction or interpretation of any provision in the Contract Documents nor affect any of the rights or obligations of the parties to the Contract.

--End--

APPENDIX D: PERFORMANCE BOND

WHEREAS the Governing Board of the Redwood Coast Montessori School ("School"), at its meeting on _____, 2022, has awarded to _____ ("Principal"), the Contract for performance of the following project ("Project"):

Heat Pumps and Solar Photovoltaic System

WHEREAS the Principal is required under the terms of the Contract to furnish a bond to the School as obligee ensuring its full and faithful performance of the Contract Documents, which are fully incorporated herein by this reference,

NOW, THEREFORE, we, the Principal and _____, as Surety, hereby guarantee the Principal's full, faithful and complete performance of the Contract Document requirements in the penal sum of _____ dollars (\$ _____) for the payment of which sum will and truly be made, we bind ourselves, our heirs, executors, administrators and successors, jointly, severally, and firmly by this agreement to perform or have performed all of the work and activities required to complete the Project pursuant to the Contract Documents and to pay to the School all damages the School incurs as a result of the Principal's failure to fully perform in accordance with the Contract Documents.

The condition of the obligation is such that if the Principal, its heirs, executors, administrators, successors or assigns shall in all things abide by, and well and truly keep and perform the covenants, conditions and agreements in the Contract Documents and any amendment thereof made as therein provided, on its or their parts to be kept and performed at the time and in the manner therein specified, and in all respects according to their true intent and meaning, and shall insure and indemnify and save harmless the School, its officers and agents, as therein stipulated, then this obligation shall become null and void. Otherwise, it shall be and remain in full force and effect.

The Surety, for value received, hereby stipulates and agrees that no change, extension of time, alteration or addition to the Contract Documents shall in any way affect its obligations on this bond and it does hereby waive notice of any such change, extension of time, alteration, or addition.

Principal and Surety further agree to pay all costs incurred by the School in connection with enforcement of this bond, including, but not limited to the School's reasonable attorney's fees and costs incurred, with or without suit, in addition to any other sum required by this bond. Surety further agrees that death, dissolution, or bankruptcy of the Principal shall not relieve the Surety of its obligations hereunder.

In witness whereof, this instrument has been duly executed by the Principal and Surety this _____ day of _____, 2022.

*To be signed by
Principal and Surety
and acknowledgment
and notarial seal to
be attached.*

PRINCIPAL

By: _____

TITLE _____

SURETY

By: _____

TITLE _____

The above bond is accepted and approved this _____ day of _____, 2022.

By: _____
Authorized School Signature

APPENDIX E: PAYMENT BOND

WHEREAS, the Redwood Coast Montessori School ("School") and the ESCO, _____ ("Principal") have entered into a contract ("Contract") for the furnishing of all materials, labor, services, equipment, tools, supervision and transportation necessary, convenient and proper for the Solar Photovoltaic System project ("Project") which Contract dated _____, 2022, and all of the Contract Documents made part thereof are fully incorporated herein by this reference; and

WHEREAS, ESCO/Principal is required by Division 4, Part 6, Title 3, Chapter 5 (commencing at Section 9550) of the California Civil Code to furnish a bond in connection with the contract;

NOW, THEREFORE, we, the ESCO/Principal and _____ as Surety, are held firmly bound unto Owner in the penal sum of \$ _____ Dollars (\$ _____), lawful money of the United States of America for the payment of which sum well and truly to be made, we bind ourselves, our heirs, executors, administrators, successors, and assigns, jointly and severally, firmly by these presents.

THE CONDITION OF THIS OBLIGATION IS SUCH that if the ESCO/Principal, his/her or its heirs, executors, administrators, successors, or assigns, or a Subcontractor, shall fail to pay any person or persons named in Civil Code Section 9100 or fail to pay for any materials or other supplies used in, upon, for, or about the performance of the work contracted to be done, or for any work or labor thereon of any kind, or for amounts due under the Unemployment Insurance Code with respect to work or labor thereon of any kind, or shall fail to deduct, withhold, and pay over to the Employment Development Department any amounts required to be deducted, withheld, and paid over by Section 13020 of the Unemployment Insurance Code with respect to work and labor thereon of any kind, then said Surety will pay for the same, in or to an amount not exceeding the amount set forth above, and in case suit is brought upon this bond Surety will also pay such reasonable attorney's fees as shall be fixed by the court, awarded and taxed as provided in Division 4, Part 6, Title 3, Chapter 5 (commencing at Section 9550) of the California Civil Code.

This bond shall inure to the benefit of any of the persons named in Section 9100 of the California Civil Code so as to give a right of action to such person or their assigns in any suit brought upon this bond. It is further stipulated and agreed that the Surety of this bond shall not be exonerated or released from the obligation of the bond by any change, extension of time for performance, addition, alteration, or modification in, to, or of any contract, plans, specifications, or agreement pertaining or relating to any scheme or work of improvement described above or pertaining or relating to the furnishing of labor, materials, or equipment therefore, nor by any change or modification of any terms of payment or extension of the time for any payment pertaining or relating to any scheme or work of improvement described above, nor by any rescission or attempted rescission of the contract, agreement, or bond, nor by any conditions precedent or subsequent in the bond attempting to limit the right of recovery of claimants otherwise entitled to recover under any such contract or agreement or under the bond, nor by any fraud practiced by any person other than the claimant seeking to recover on the bond, and that this bond be construed most strongly against the Surety and in favor of all persons for whose benefit such bond is given, and under no circumstances shall Surety be released from liability to those for whose

benefit such bond has been given, by reason of any breach of contract between the Owner and original ESCO or on the part of any obligee named in such bond, but the sole conditions of recovery shall be that claimant is a person described in Section 8400 and 8402 of the California Civil Code and has not been paid the full amount of his/her or its claim and that Surety does hereby waive notice of any such change, extension of time, addition, alteration, or modification.

In witness whereof, this instrument has been duly executed by the Principal and Surety this _____ day of _____, 2022.

*To be signed by
Principal and Surety
and acknowledgment
and notarial seal to
be attached.*

PRINCIPAL

By: _____

Title

SURETY

By: _____

Title

The above bond is accepted and approved this _____ day of _____, 2022.

By: _____
Authorized School Signature

APPENDIX F: WARRANTY BOND

KNOW ALL PERSONS BY THESE PRESENTS, that

WHEREAS the Redwood Coast Montessori School (“School”) and the contractor _____, (“Principal”) have entered into a Contract (“Contract”) for the following project (Project):

Heat Pump and Solar Photovoltaic System

WHEREAS, Principal is required under the terms of the Agreement to furnish warranty security for the work performed pursuant to the Agreement in the amount of \$ _____ to guarantee replacement and repair of the improvements as described in the Agreement for a period of one year following the date of recordation of the notice of acceptance of the Improvements against any defective work or labor done, or defective materials furnished.

NOW, THEREFORE, we, the Principal, and _____ as Surety, are held and firmly bound unto the School in the penal sum of _____ Dollars (\$ _____) lawful money of the United States, being not less than 10 percent (10%) of the amount payable by the terms of the Contract, for the payment of which sum well and truly to be made we bind ourselves, our heirs, executors, administrators and successors, jointly and severally, firmly by these presents.

The condition of this obligation is such that if Principal shall indemnify School for all loss that School may sustain by reason of any defective materials or workmanship which become apparent during the period of one year from and after acceptance of the improvements by the School Council of School, then this obligation shall be null and void; otherwise, this obligation shall remain in full force and effect.

As a part of the obligation secured hereby and in addition to the face amount specified, costs and reasonable expenses and fees shall be included, including reasonable attorneys’ fees incurred by School in successfully enforcing the obligation, all to be taxed as costs and included in any judgment rendered.

Surety’s obligations hereunder are independent of the obligations of any other surety for the performance of the Contract, and suit may be brought against Surety and such other sureties, jointly and severally, or against any one or more of them, or against less than all of them without impairing the School’s rights against the others.

No right of action shall accrue on this bond to or for the use of any person or corporation other than the School or its successors or assigns.

Surety shall provide School with thirty (30) days’ written notice of Principal’s default prior to Surety terminating, suspending, or revoking the bond.

The Surety hereby stipulates and agrees that no change, extension of time, alteration, or addition to the terms of the Contract or to the work to be performed there under or the Specifications accompanying the same shall in any way affect its obligation on this bond, and it does hereby waive

notice of any such change, extension of time, alteration, or addition to the terms of the Contract or to the work or to the Specifications.

IN WITNESS WHEREOF, the above-bound parties have executed this instrument under their seals this _____ day of _____, 2022, the name and corporate seal of each corporate body being hereto affixed, and these presents duly signed by its undersigned representative, pursuant to authority of its governing body.

*To be signed by
Principal and Surety
and acknowledgment
and notarial seal to
be attached.*

PRINCIPAL

By: _____

TITLE _____

SURETY

By: _____

TITLE _____

The above bond is accepted and approved this _____ day of _____, 2022.

By: _____
Authorized School Signature

Print Name & Title

APPENDIX G: SUBCONTRACTOR LIST FORM

Each bidder shall list below the name and location of place of business for each Subcontractor who will perform a portion of the Contract work in an amount in excess of 1/2 of 1 percent of the total contract price. The nature of the work to be subcontracted shall also be described. Per SB96 Public Contract Code 4104, please list the DIR registration number for each Subcontractor.

[illegible]

APPENDIX H: TECHNICAL FACILITY PROFILE

The information in this technical facility profile is provided to inform the proposer about the facilities.


Operating Information

The School requests that the installation take place during school breaks. The scheduled breaks are as follows:

- Summer Break 2022: June 16 to August 26, 2022
- Thanksgiving Break 2022: November 21-25, 2022
- Winter Break 2022: December 19-30, 2022


Proposed PV Location

Screen shot from Google Maps for Redwood Coast Montessori School, 1611 Peninsula Dr, Arcata (Manila), CA 95521

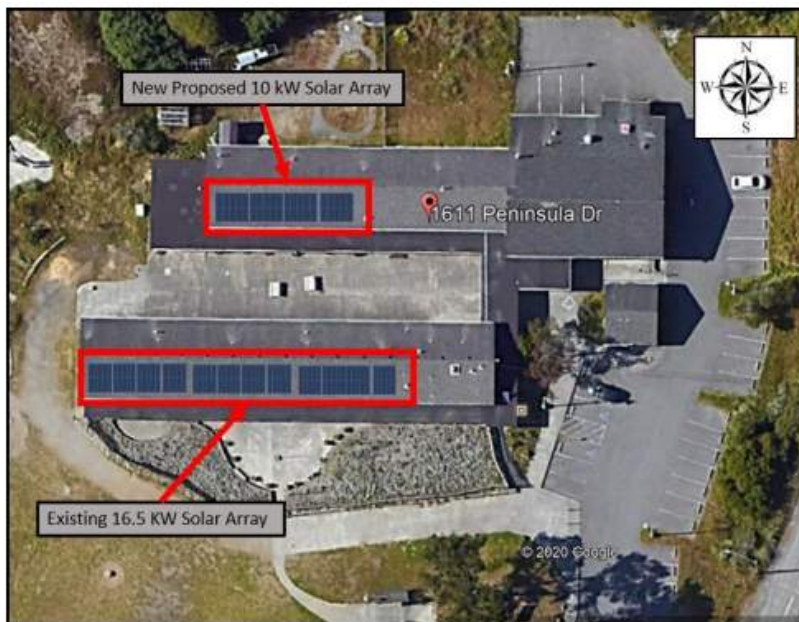


Existing Heaters

Unit Location	Areas Served	SF Served	Make	Model	BTU/h
Office F	Office F	576	Rinnai	EX08CP	6400
Copy Room	Copy Room and Offices K and L	600	Rinnai	EX08CP	6400
Classroom I	Classroom H and I	1888	RUUD	RGPS-07EAMER	60000
Room J	Community Center (Room J)	951	Luxaire	TG8S040A08MP11B	32000
MPR	MPR	3360	Reznor	Unknown	64000
Classroom E	Classroom E and Classroom D	1895	RUUD	RGPS-07EAMER	60000
Classroom C	Classroom B and Classroom C	1888	RUUD	RGPS-07EAMER	60000

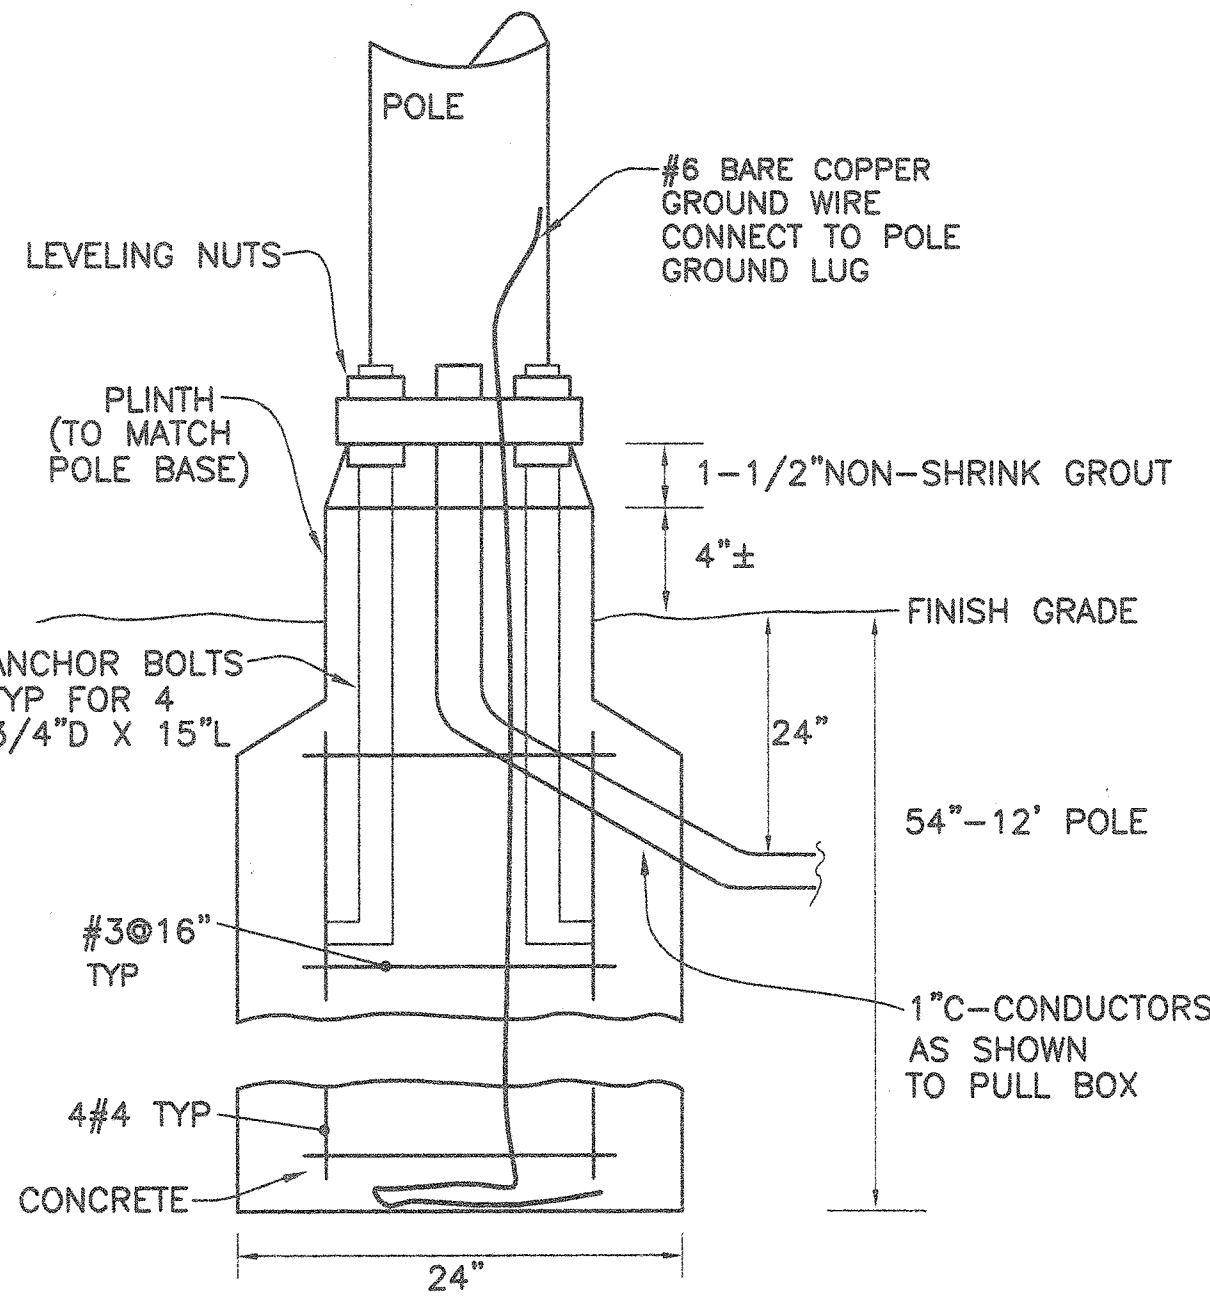


FIXTURES 'C' POLE BASE

NOTE
COORDINATE WITH POLES
SUPPLIED FOR THIS PROJECT

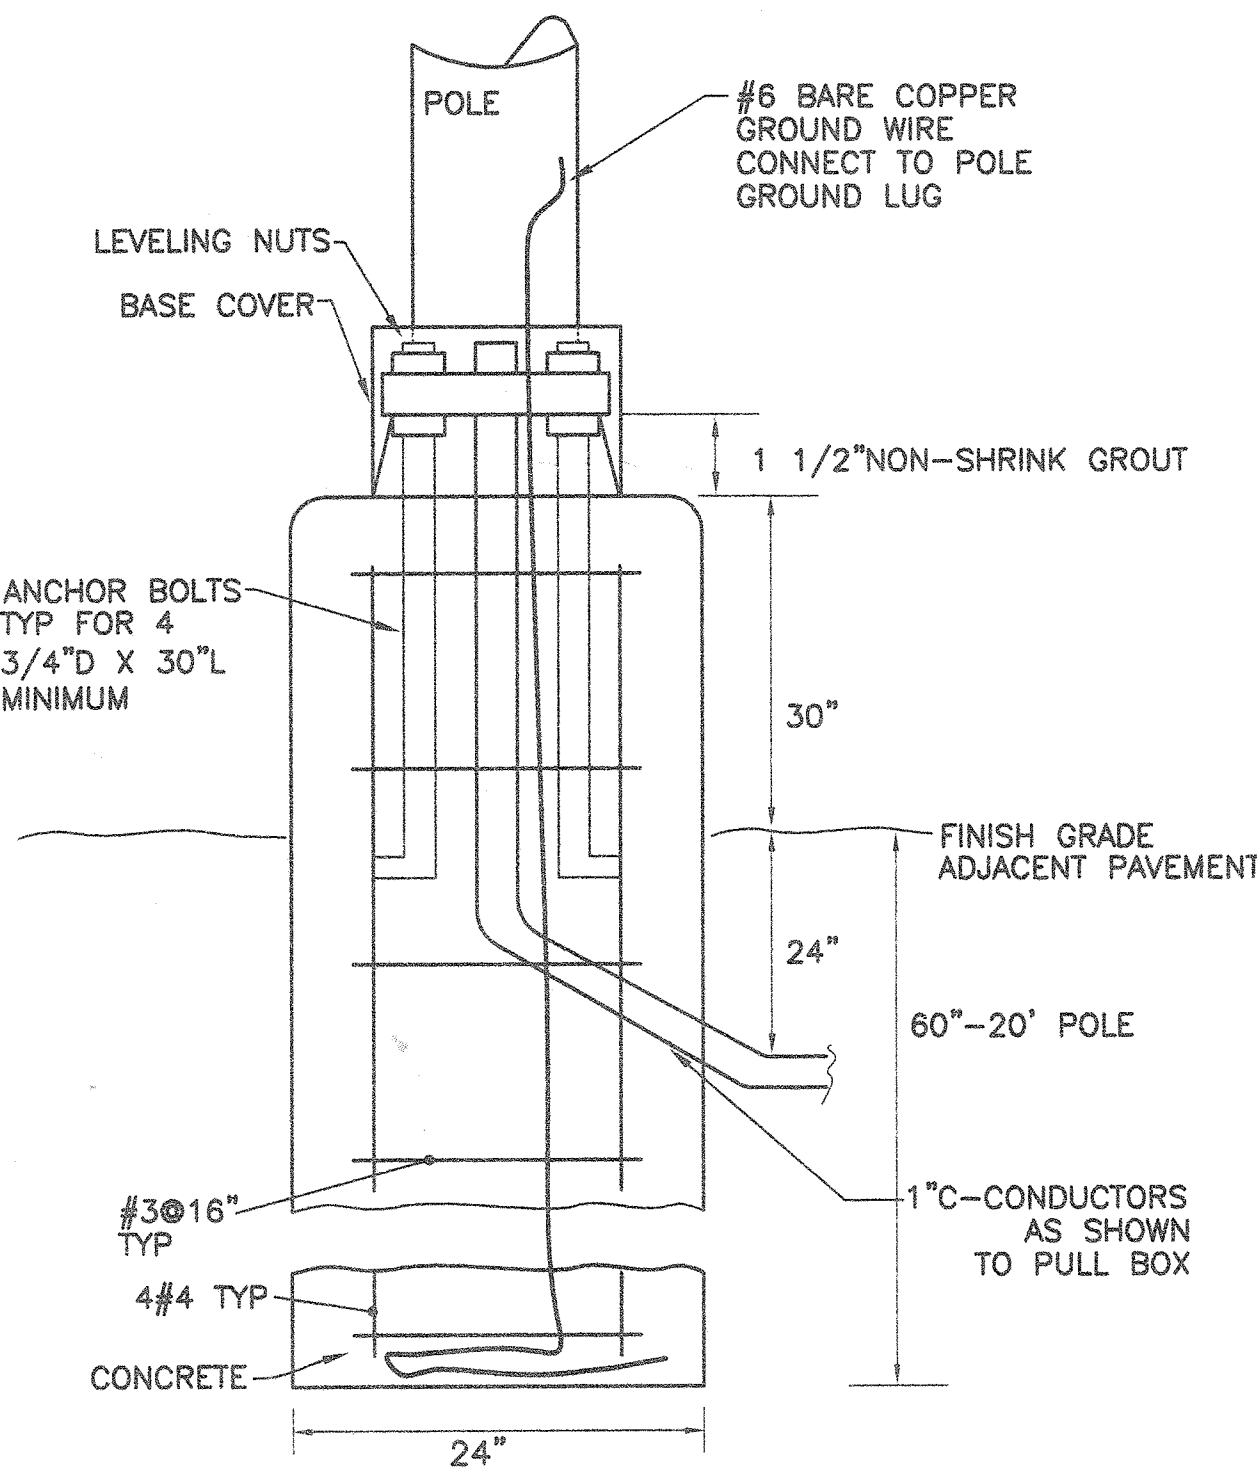

FIXTURES 'A' & 'B' POLE BASE

NOTE
COORDINATE WITH POLES
SUPPLIED FOR THIS PROJECT

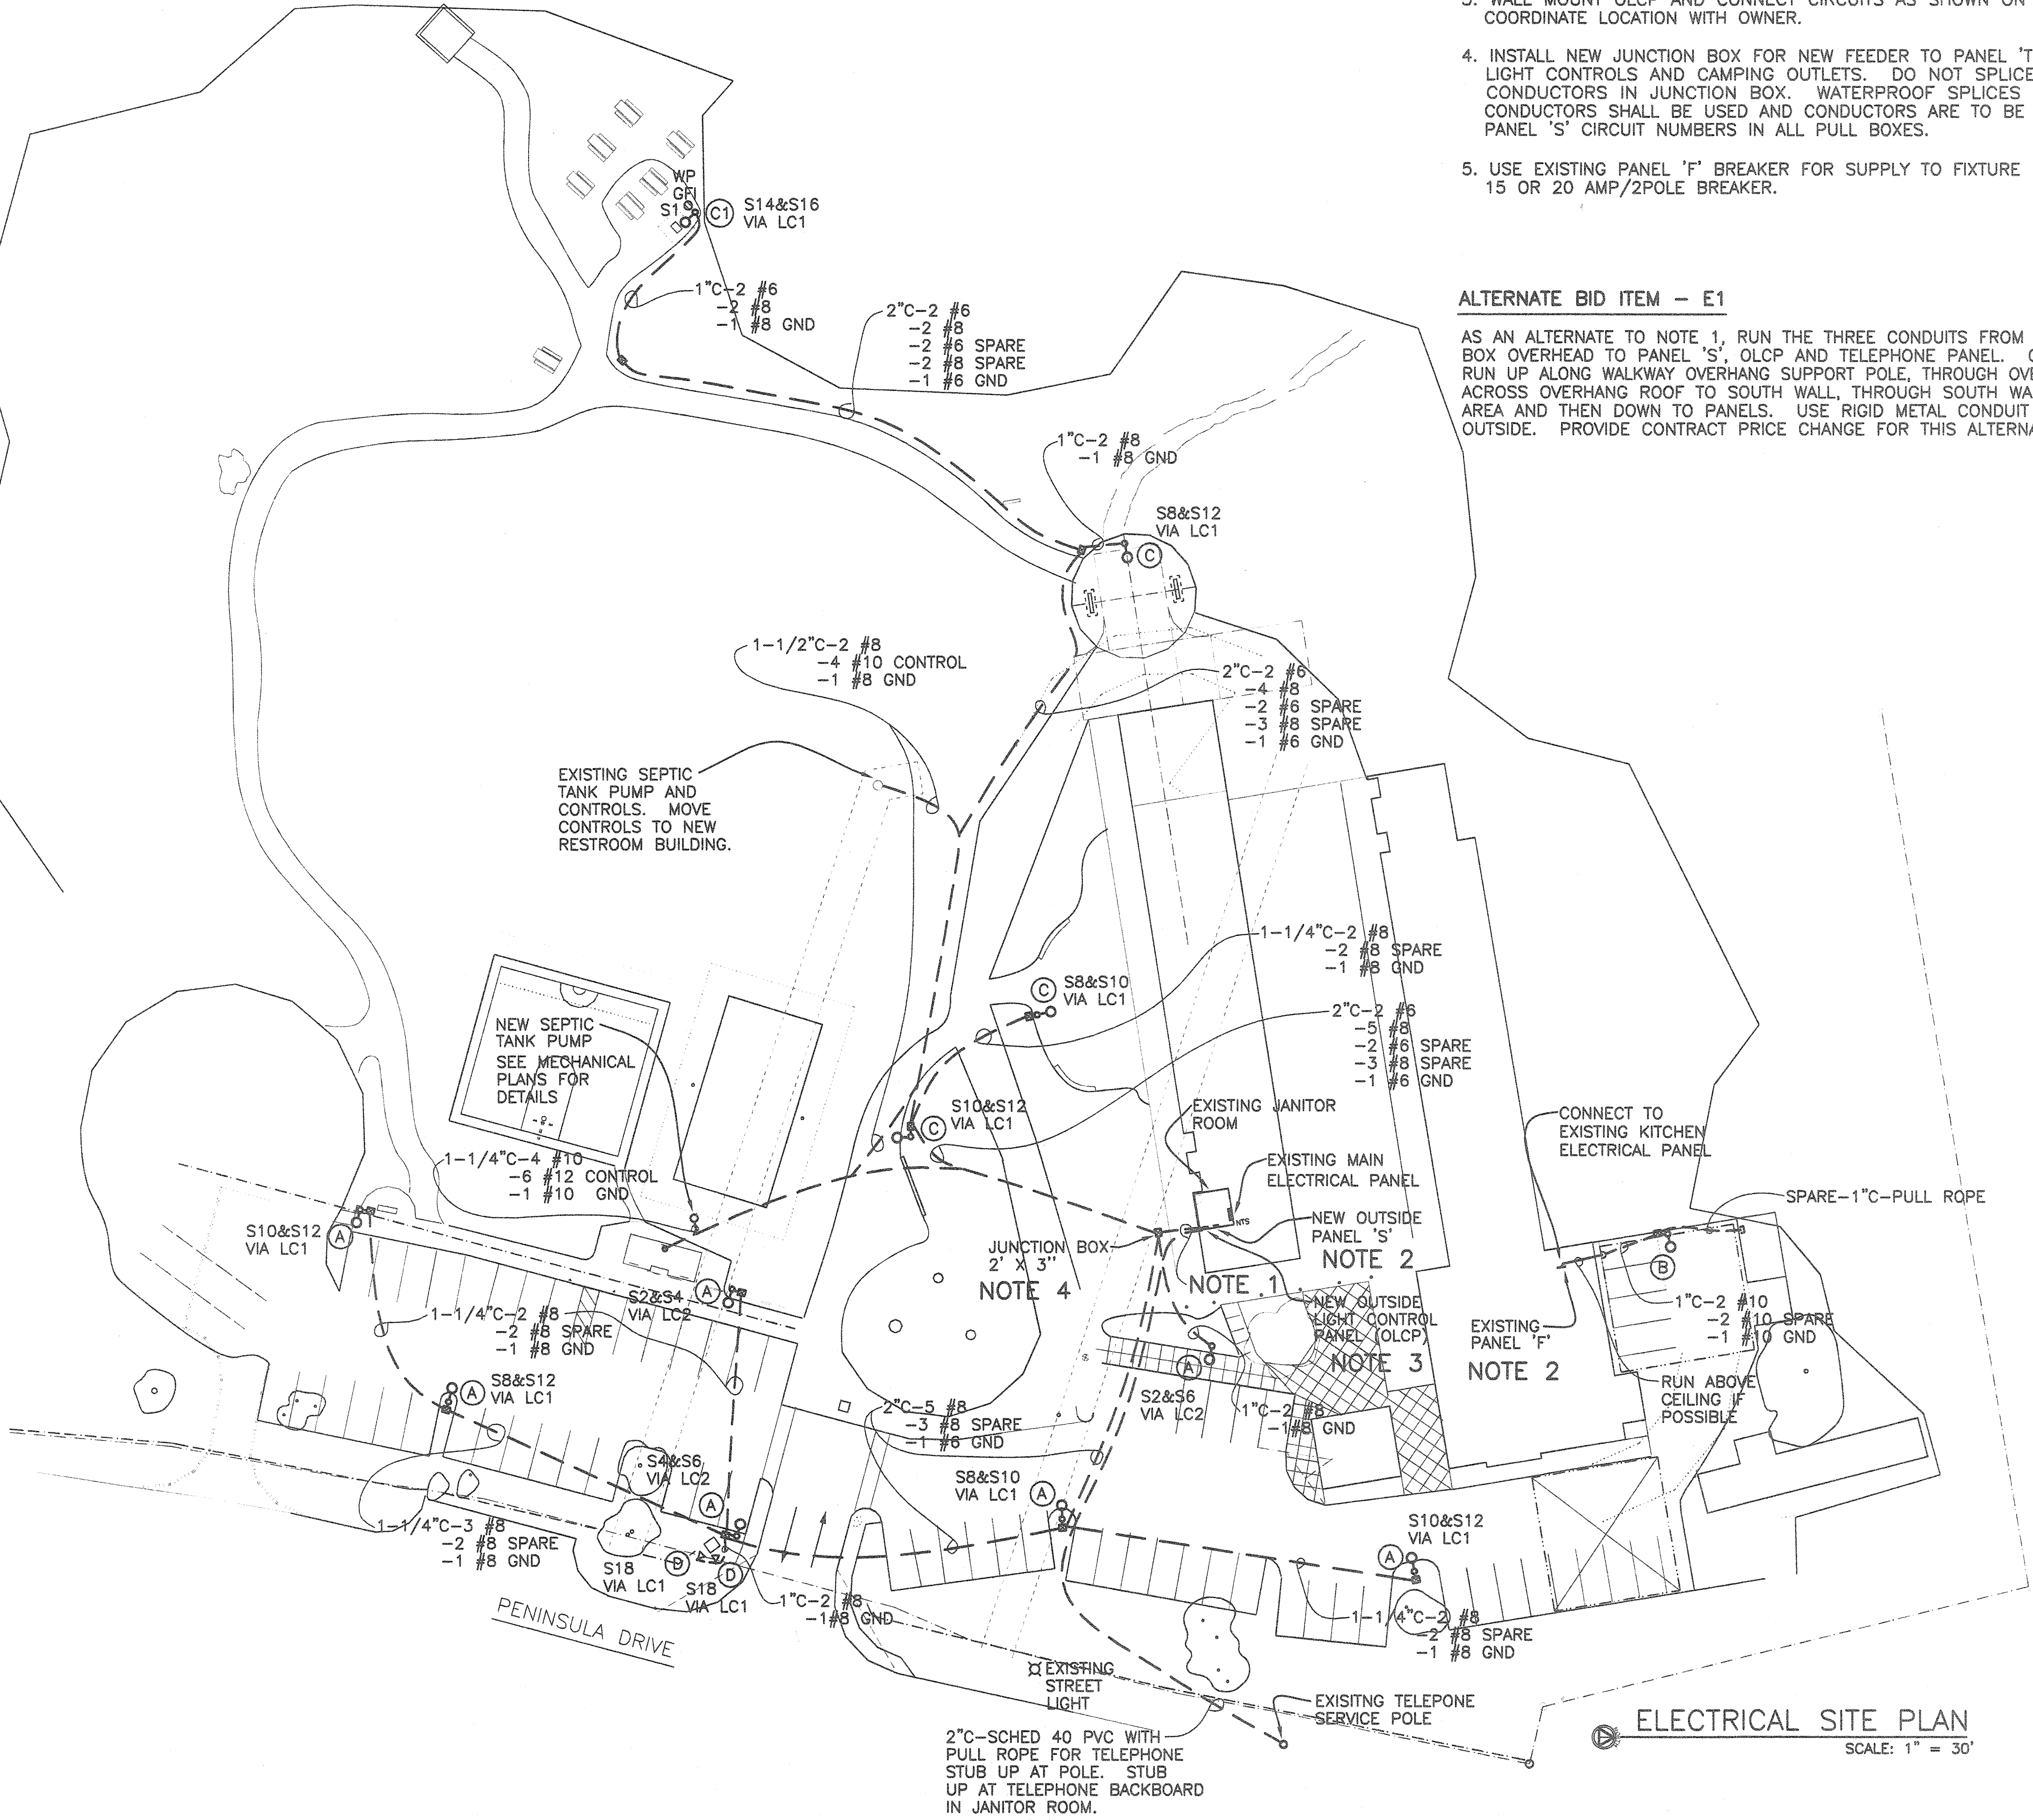


NOTES:

1. SAWCUT EXISTING WALKWAY, CORE DRILL THROUGH EXISTING FOUNDATION AND OPEN CONCRETE FLOOR IN JANITOR ROOM TO INSTALL NEW CONDUITS SHOWN (3). REPAIR FLOOR AND WALKWAY TO ORIGINAL CONDITION AFTER INSTALLATION OF CONDUITS AND COMPACTED BACKFILL. EXTEND CONDUITS UP TO PANELS.
2. WALL MOUNT PANEL IN EXISTING JANITOR ROOM. RUN PANEL 'S' FEEDER UP THROUGH TOP OF EXISTING MAIN SERVICE PANEL INTO ATTIC SPACE. ROUTE SOUTH TO PANEL 'S' AND THEN DOWN THROUGH CEILING AND CONNECT TO TOP OF PANEL 'S'. COORDINATE LOCATION WITH OWNER.
3. WALL MOUNT OLCP AND CONNECT CIRCUITS AS SHOWN ON DWG. #E2. COORDINATE LOCATION WITH OWNER.
4. INSTALL NEW JUNCTION BOX FOR NEW FEEDER TO PANEL 'T', OUTSIDE LIGHT CONTROLS AND CAMPING OUTLETS. DO NOT SPLICE FEEDER 'T' CONDUCTORS IN JUNCTION BOX. WATERPROOF SPLICES FOR LIGHTING CONDUCTORS SHALL BE USED AND CONDUCTORS ARE TO BE LABELED WITH PANEL 'S' CIRCUIT NUMBERS IN ALL PULL BOXES.
5. USE EXISTING PANEL 'F' BREAKER FOR SUPPLY TO FIXTURE (B). USE 15 OR 20 AMP/2POLE BREAKER.

ALTERNATE BID ITEM - E1

AS AN ALTERNATE TO NOTE 1, RUN THE THREE CONDUITS FROM THE JUNCTION BOX OVERHEAD TO PANEL 'S', OLCP AND TELEPHONE PANEL. CONDUITS TO RUN UP ALONG WALKWAY OVERHANG SUPPORT POLE, THROUGH OVERHANG ROOF, ACROSS OVERHANG ROOF TO SOUTH WALL, THROUGH SOUTH WALL TO ATTIC AREA AND THEN DOWN TO PANELS. USE RIGID METAL CONDUIT EXPOSED OUTSIDE. PROVIDE CONTRACT PRICE CHANGE FOR THIS ALTERNATE.

TRAVIE J. WESTLUND, P.E.
2603 S STREET
EUREKA, CA 95501
TELEPHONE 707/442-6256
FAX 707/442-0555



ELECTRICAL SITE PLAN
MANILA DUNES RECREATION AREA
COMMUNITY CENTER
MANILA, CALIFORNIA

SCALE: NOTED

E1

LMAN LA
FILE: W117BASE
4/18-02
